



Project Online | **Data Migration**

July 2026



Contents

01

Overview

02

Project Schedules

03

Project Online Data

04

Project Online |
Timesheets

05

Project Online |
Portfolio Analyses

06

SharePoint Online |
List Data

07

SharePoint Online |
Documents

08

Support



Data Migration Overview

Overview

What is the reason for this project?

Project Online Retirement | Microsoft is retiring Project Online in September 2026. There is a limited time window to develop tools to assist our Customers with migrating from Project Online to Altus.

Migration Tools Required | The Altus team will need to develop tools to provide a simple and easy way for Customers to get their content out of Project Online and into Altus.


Opportunity to Increase Customers | The retirement of Project Online presents us with a unique opportunity to obtain additional Customers and Partners around the globe and provide them with a fantastic PPM experience.

Data Migration | This pack is focused only on the data migration activities. Configuration and Altus features will need to be considered as part of the product development process.

Project Online & SharePoint Online data

What data do Customers need to get from Project Online and SharePoint Online?

The following data will need to be extracted from both Project Online and SharePoint Online



High-Level Scope

What will the data migration project involve?

The Altus approach is designed to migrate data from a 'standard' Project Online environment. Empower and Reporting Hub customers can utilise an alternative approach for list, project, and resource data. Please speak to your Sensei account managers for further information here.

In Scope

Data Migration Tools | The Altus team will configure scripts and develop tools to assist customers in moving their data from Project Online to Altus.

Technical Documentation | Will be created to document how scripts work and can be run and will specify exactly what data will be migrated.

Migration Assistance | Altus will aid customers when using the tools we have developed to migrate data from Project Online.

Altus onboarding | Customers will be assisted with their onboarding activities as part of customer activation provided by the Customer Success lead.

Out of Scope

Altus Feature Development | Whilst the Altus team will continue working on feature development, that is not in scope for the data migration project.


Altus Customization | The data migration is focused on getting customer data in to the out-of-the-box Altus solution. No solution customization will be undertaken.

Non-sub site list data | The data migration will focus on moving customers from a standard implementation of Project Online and will only grab data from SharePoint sub-sites.

Microsoft licensing | Whilst we have guidance on the licensing required, it will be the onus of the customer to ensure they have sufficient licensing to support them.

👤 Roles & Responsibilities | Project Team

Who will be involved in the data migration, and what will they be responsible for?



Roles & Responsibilities | Project Team

Who will be involved in the data migration, and what will they be responsible for?

Role	Responsibilities
Sponsor Marc Soester	▪ Make decisions on scope and priority order. ▪ Set the deadline dates and set expectations for the outcomes.
Initiative Lead John Price	▪ Manage risks, issues, dependencies, and change control. ▪ Oversee quality assurance and key sign-off processes. ▪ Set the scope and priority order.
Delivery Manager Robert Setiadi	▪ Define and manage the delivery timelines and scrum processes. ▪ Identify suitable resources for the work and determine their availability to work on the scope items. ▪ Manage the allocations and Azure Dev Ops processes.
Developers Robert to confirm	▪ Analyse Project Online and SharePoint Online structures to understand how data can be extracted. ▪ Build scripts and tools to extract information from the source systems. ▪ Optimise the performance of the migration process to handle large volumes of data. ▪ Collaborate with the test analysts to resolve defects and define the data extract methods.
Test Analysts Robert to confirm	▪ Define the test plans and test scenarios for the data migration. ▪ Identify required test data and prepare test environments. ▪ Execute data validation and performance test cases. ▪ Log defects and work with the developers to resolve.
Adoption Lead Francis Luzuriaga	▪ Provide training materials which cover how to guides regarding how to complete Project Online activities within Altus. ▪ Assist the project manager with other materials which are required to assist Partners and Customers with their Project Online migration activities.


Roles & Responsibilities | Key Stakeholders

What stakeholders will be interested in the Project Online migration?

Stakeholder	Involvement
Product Managers	▪ Will want to know when the migration scripting work is required to be completed by. ▪ The work will need to be completed by Altus developers so will impact their availability for Altus features and bug resolution work.
Partners & Customers	▪ Will be wanting the details of the Altus project online migration approach and tools. ▪ They will be able to participate in User Acceptance Testing (UAT) to ensure that the tools are fit for purpose and provide the required outcome.

↑ Scope MoSCoW Priority

What is the priority for data migration scope? This has been prioritised using a MoSCoW approach.

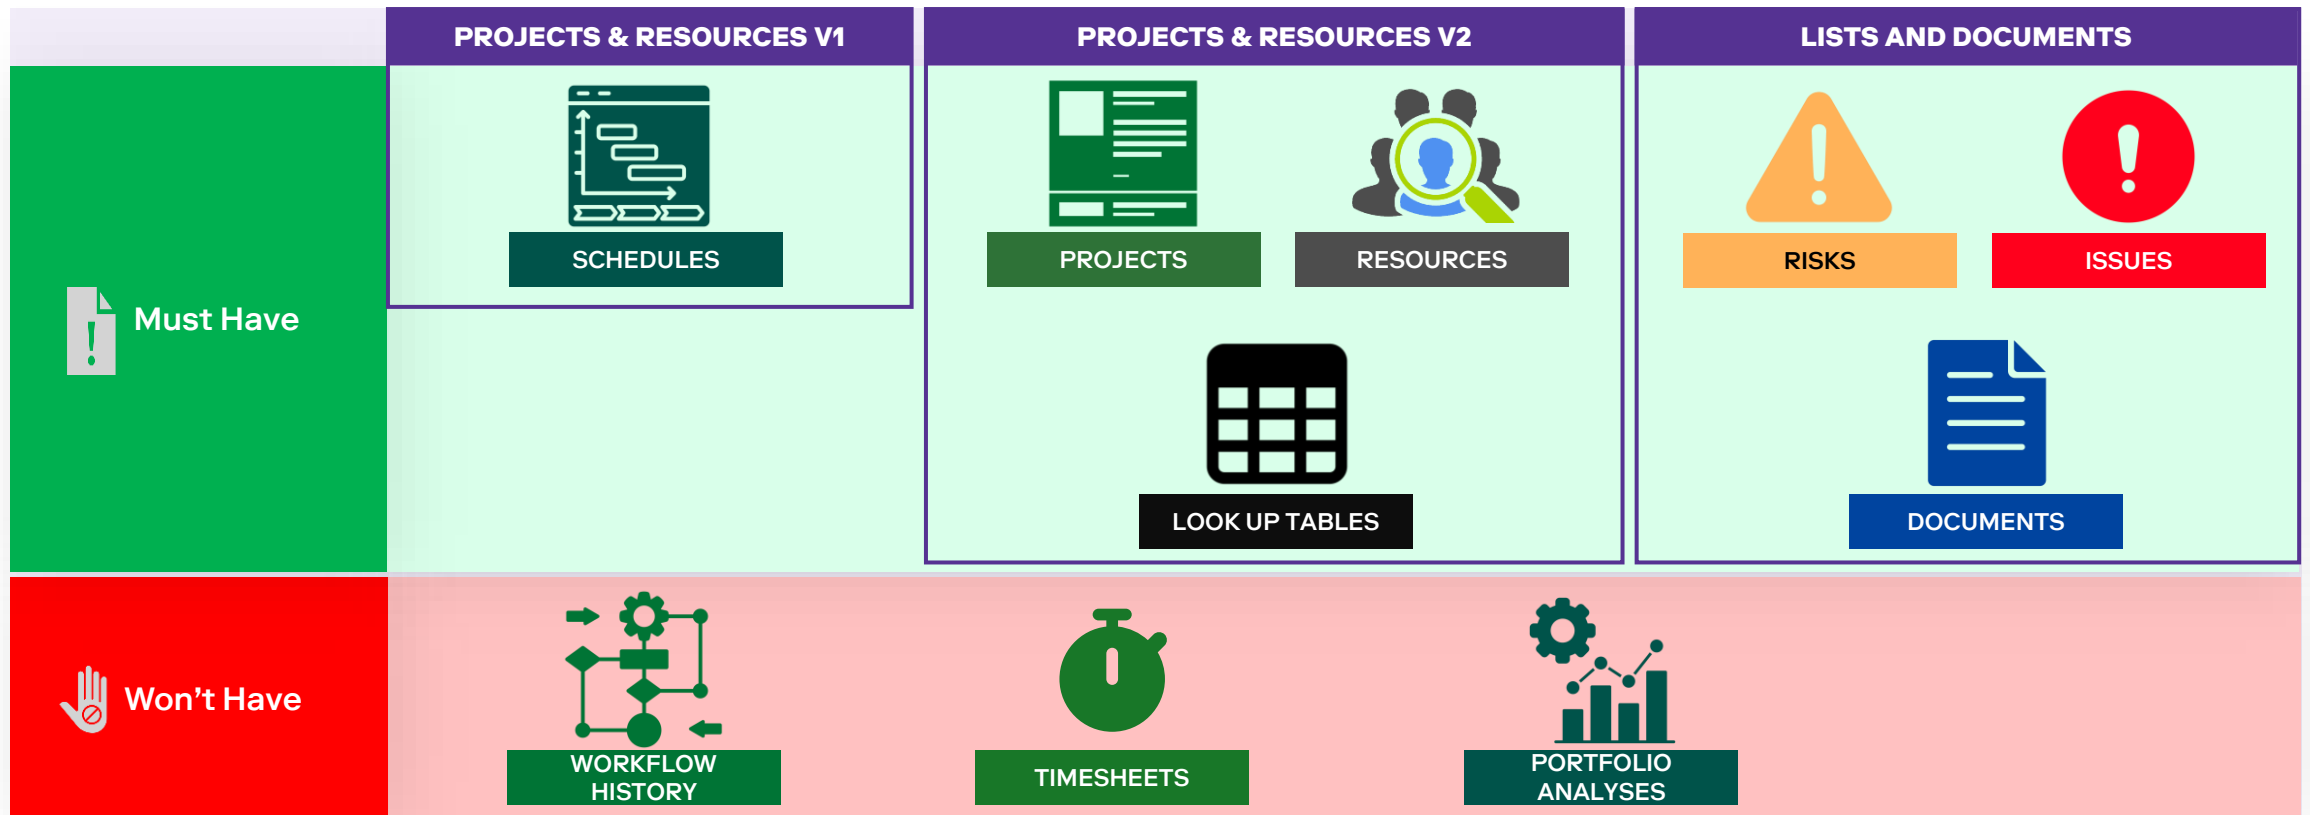

High-Level Timeline for Migration tools

When will we provide data migration tools to our Partners and Customers?

- Below are the indicative dates for the tooling work we're doing for the project online data migration.
- We are working to have everything finalised at the end of Q1-2026 so that Partners and Customers have time to run their migrations before the September cut off.

2026	QUARTER 1			QUARTER 2			QUARTER 3			QUARTER 4		
	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
PROJECTS & RESOURCES V1	ROLL OUT		SUPPORT									
PROJECTS & RESOURCES V2	BUILD	TEST	ROLL OUT	SUPPORT								
SHAREPOINT LIST DATA & DOCUMENTS	DESIGN	BUILD	TEST	ROLL OUT	SUPPORT							

Project Online decommissioned | 30th Sept 2026


The background of the slide is a photograph of a modern office interior. Three people are seated in a lounge area with large windows. A man is sitting on a black leather sofa, looking at a tablet. A woman and a man are sitting on the floor, looking at a laptop on a low table. The room has large windows that look out onto a green landscape and a modern building. The overall atmosphere is professional and collaborative.

Data Migration Schedules

Schedule Migration

What data do Customers need to get from Project Online?


Project schedules need to be extracted from Project Online.

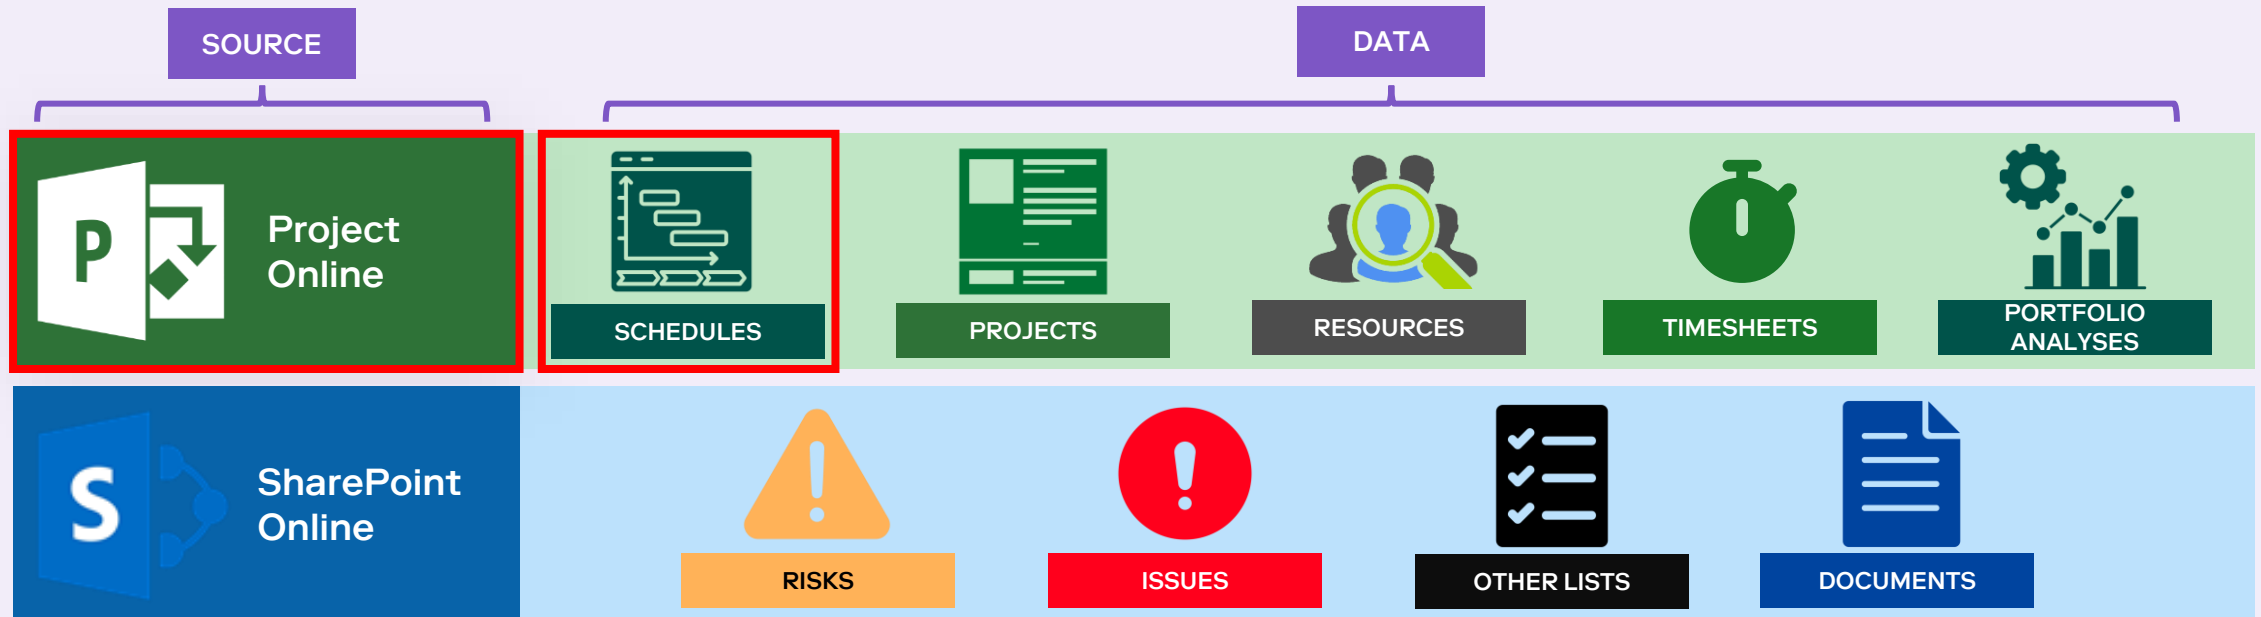

►► Schedule Migration | Approach

How will schedules be migrated to Altus?

The diagram below outlines the high-level process for migrating schedules to Altus.

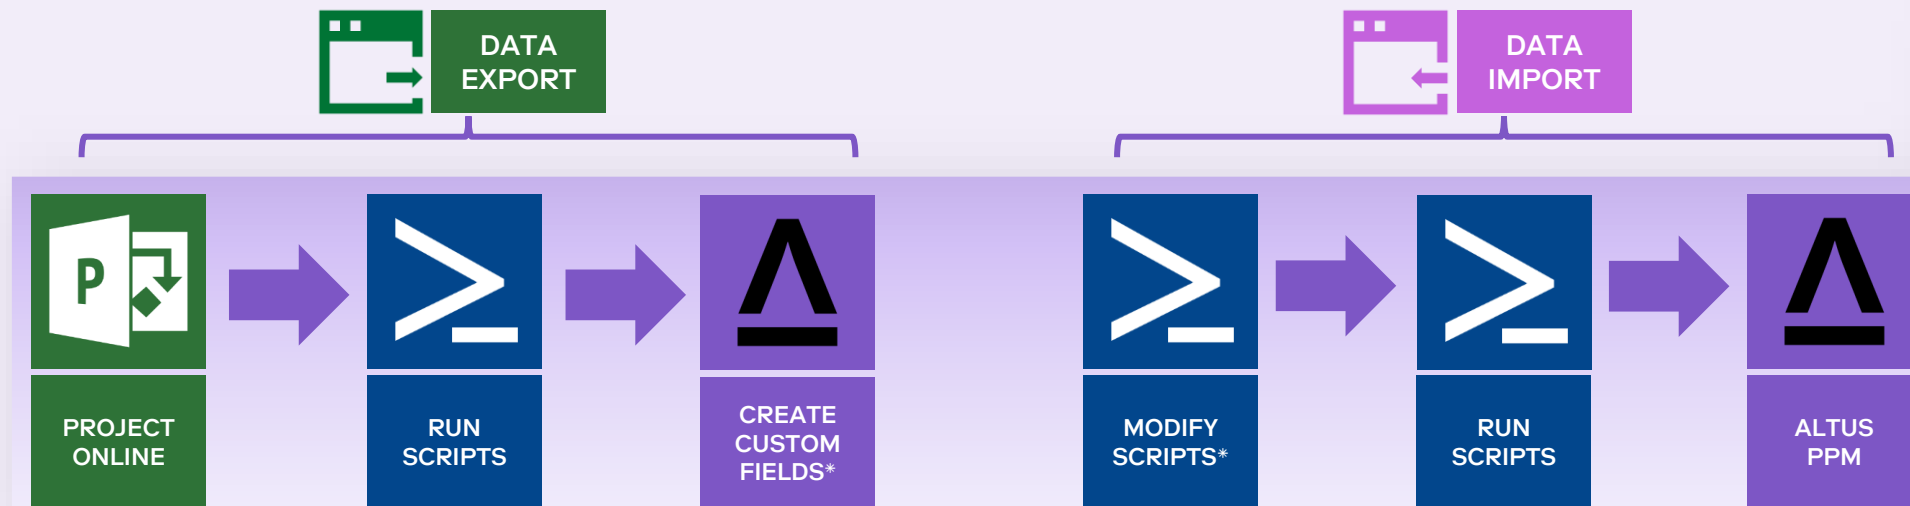


*Altus scripts can be modified to include custom fields and lookup tables. The scripts map the data between Project Online and Altus to mitigate the need for a manual migration of this data between systems.

►► Schedule Migration | Approach

How will schedules be migrated to Altus?

The diagram below outlines the high-level process for migrating schedules to Altus.

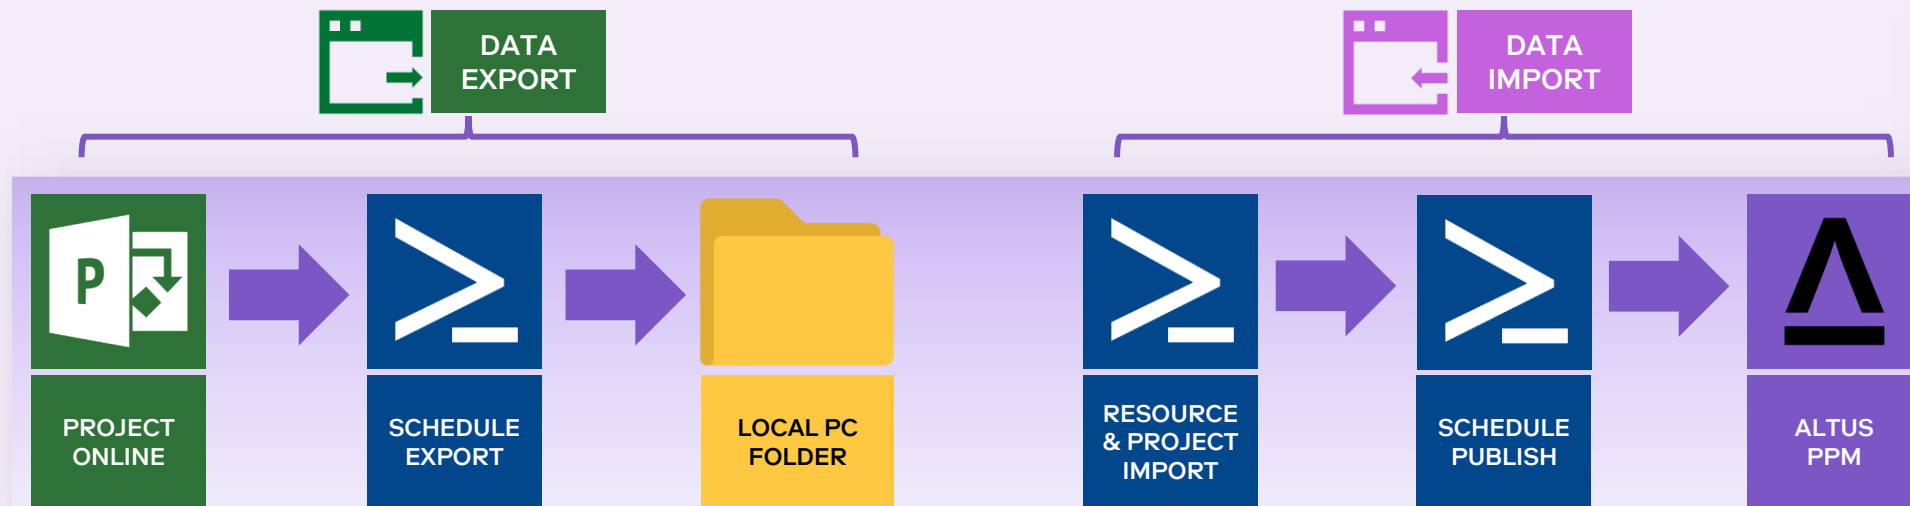

Microsoft scripts enable customers to extract data from Project Online.




Altus scripts enable customers to import project online data into Altus.

►► Schedule Migration | Approach

How will schedules be migrated to Altus?


The diagram below outlines the high-level process for migrating schedules to Altus.

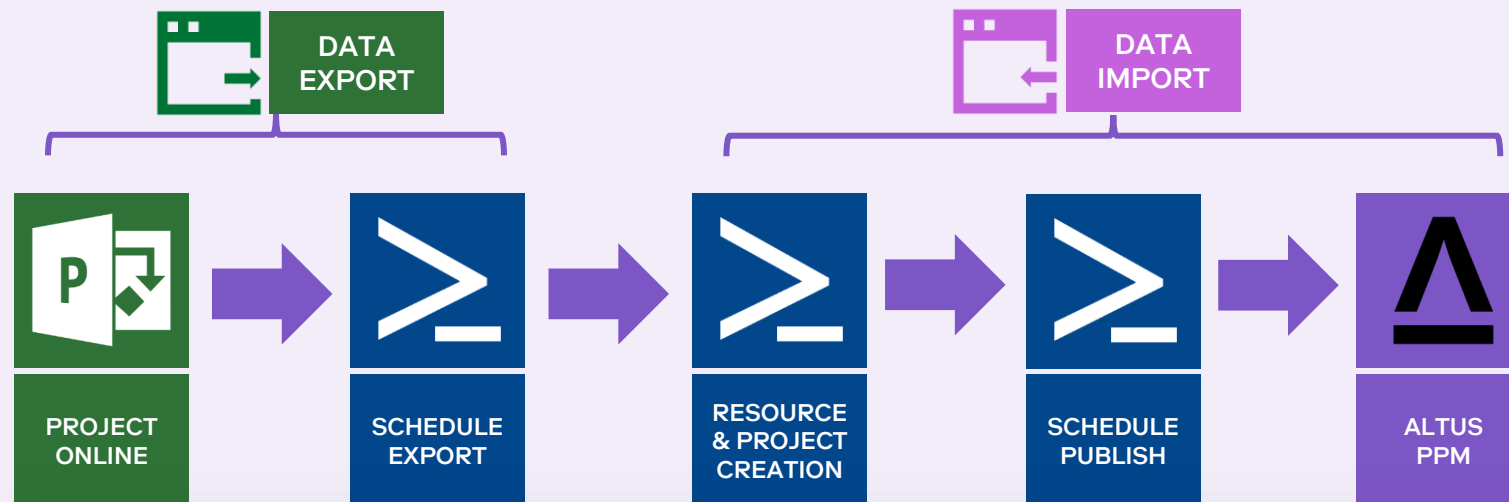

Process enables an automated migration of data from Project Online to Altus PPM. This process is robust and provides a complete end-to-end solution for migrating Projects, Resources & Schedules.

Schedule Migration | Scope

What data will and won't be migrated into Altus by the schedule migration scripts?

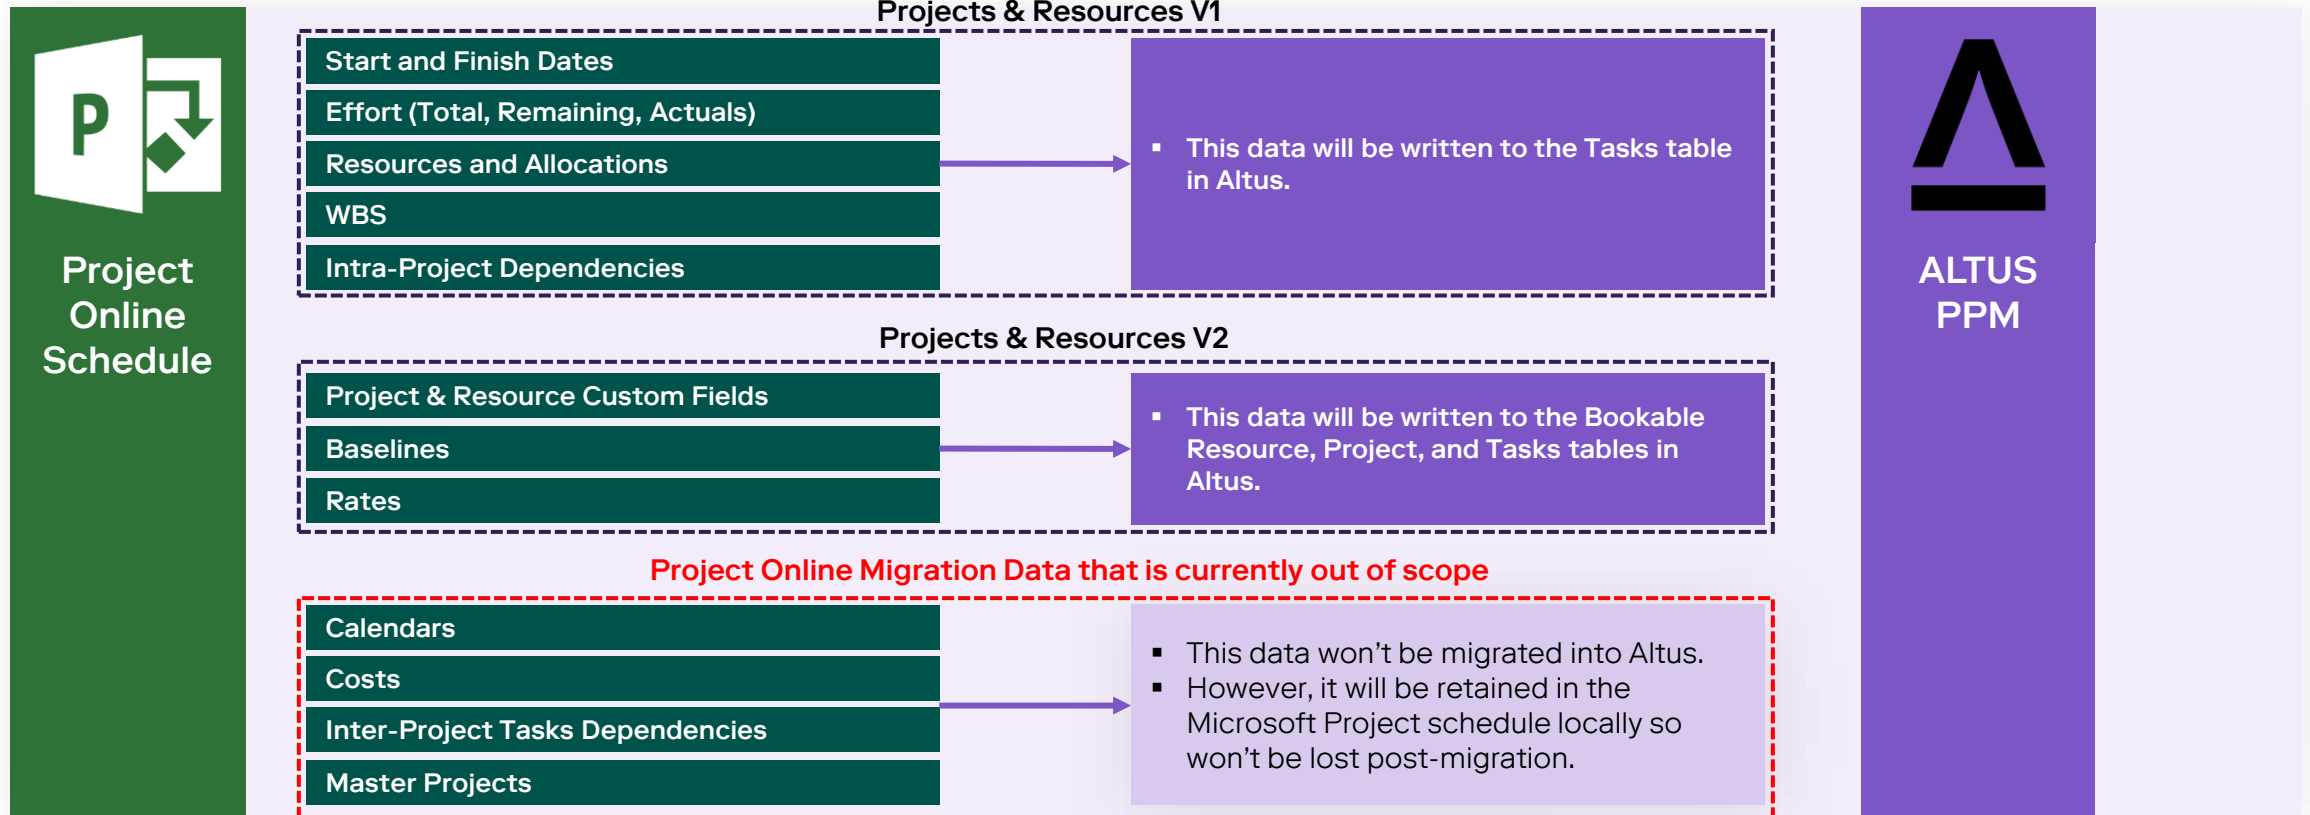

Schedule Migration | Scope

What data will be migrated by the Altus schedule migration scripts?

In Scope

Project Creation

- Create projects in Altus based on the Project Online schedule that has been exported from Project Online.
- Note, this will create a 'shell record' with minimum data requirements to create the project in Altus.

Bookable Resource Creation

- Create Bookable Resources in Altus based on the Project Online schedule resource pool that has been exported from Project Online.
- Note, this will create a 'shell record' with minimum data requirements to create the bookable resource in Altus.

Schedule Data

- When project online schedules are migrated into Altus, this will populate all the fields in the Altus tasks table.
- This will include the following data: Dates, Effort, Resources (and Allocations), Dependencies (Predecessors and Successors), WBS structure.

Schedule Migration | Scope

What data won't be migrated by the Altus schedule migration scripts?

Out of Scope (*at the time of writing*)

Baselines	▪ Baselines from the Project Schedule won't be created in Altus. ▪ Baseline data within them will be retained in the Microsoft Project schedule.
Resource Custom Fields	▪ Any resource custom fields that have been created in Microsoft Project won't be created in Altus and no data will be migrated. ▪ These fields and the data within them will be retained in the Microsoft Project schedule.
Project Custom Fields	▪ Any custom fields that have been created in Project Online won't be created in Altus and no data will be migrated. ▪ These fields and the data within them will be retained in the Microsoft Project schedule.
Resource Rates	▪ Resource rates that have been set in Microsoft Project won't be migrated to Altus. ▪ This data will be retained in the Microsoft Project schedule.
Calendars	▪ Project Calendars that have been created in Microsoft Project won't be migrated to Altus. ▪ This data will be retained in the Microsoft Project schedule.
Task Custom Fields	▪ Any task custom fields that have been created in Microsoft Project won't be created in Altus and no data will be migrated. ▪ These fields and the data within them will be retained in the Microsoft Project schedule.

Schedule Migration | Scope

What data won't be migrated by the Altus schedule migration scripts?

Out of Scope (*at the time of writing*)

Costs

- Costs from the Project Schedule won't be created in Altus.
- Cost data within them will be retained in the Microsoft Project schedule.


Schedule Migration | Pre-requisites

What software is required to run the end-to-end schedule migration process?

Pre-requisite	Details
Altus for Project	▪ The process requires our desktop application, Altus for Project to be installed. ▪ You can download this application via this link: ▪ https://project.altus.pro/AltusAddinSetup.msi
PowerShell 7.4	▪ The user will need to have PowerShell 7.4 (or higher) on their PC. ▪ You can download this version via this link: ▪ https://learn.microsoft.com/en-us/powershell/scripting/install/install-powershell-on-windows?view=powershell-7.5
Azure PowerShell Module 11.1.0	▪ Once you have PowerShell 7.4 installed, open Windows PowerShell and run these commands to install the Azure PowerShell Module 11.1.0: ▪ <code>Install-Module -Name PowerShellGet -Force</code> ▪ <code>Install-Module -Name Az -RequiredVersion 11.1.0 -Scope AllUsers</code>
Licenses	▪ The user running the scripts will need a Project Online and Project Desktop License (P3 or above). ▪ The user will also need the following Microsoft licences for Altus: Technical readiness Altus Docs
O365 Groups	▪ Partners and Customers will need to create all O365 Groups for the SharePoint Documents migration. ▪ The exception here will be if the Partners opts to move the entire SharePoint Site Collection.

Schedule Migration | End-to-end process


The diagram below articulates the steps in the end-to-end process for the schedule migration.

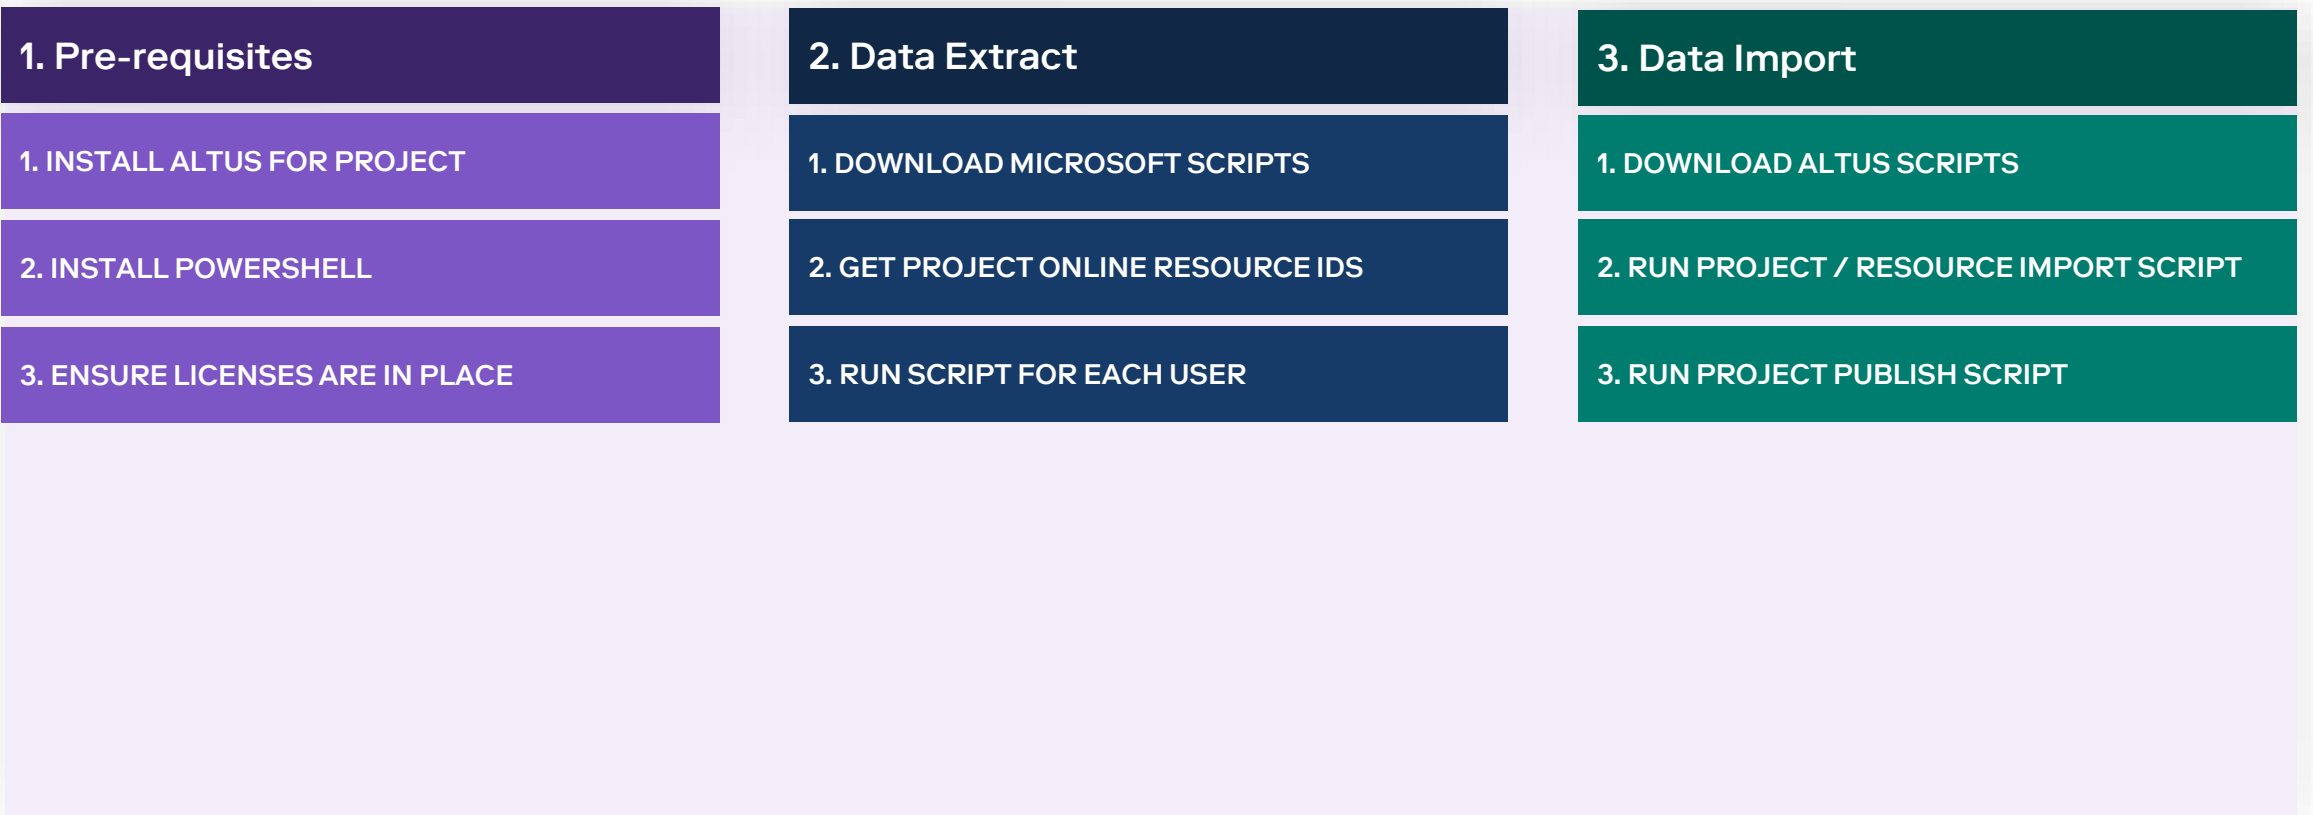

</> Microsoft Script | .MPP file extract

Creation of .MPP files for project schedules stored in Project Online.


.MPP extraction from Project Online

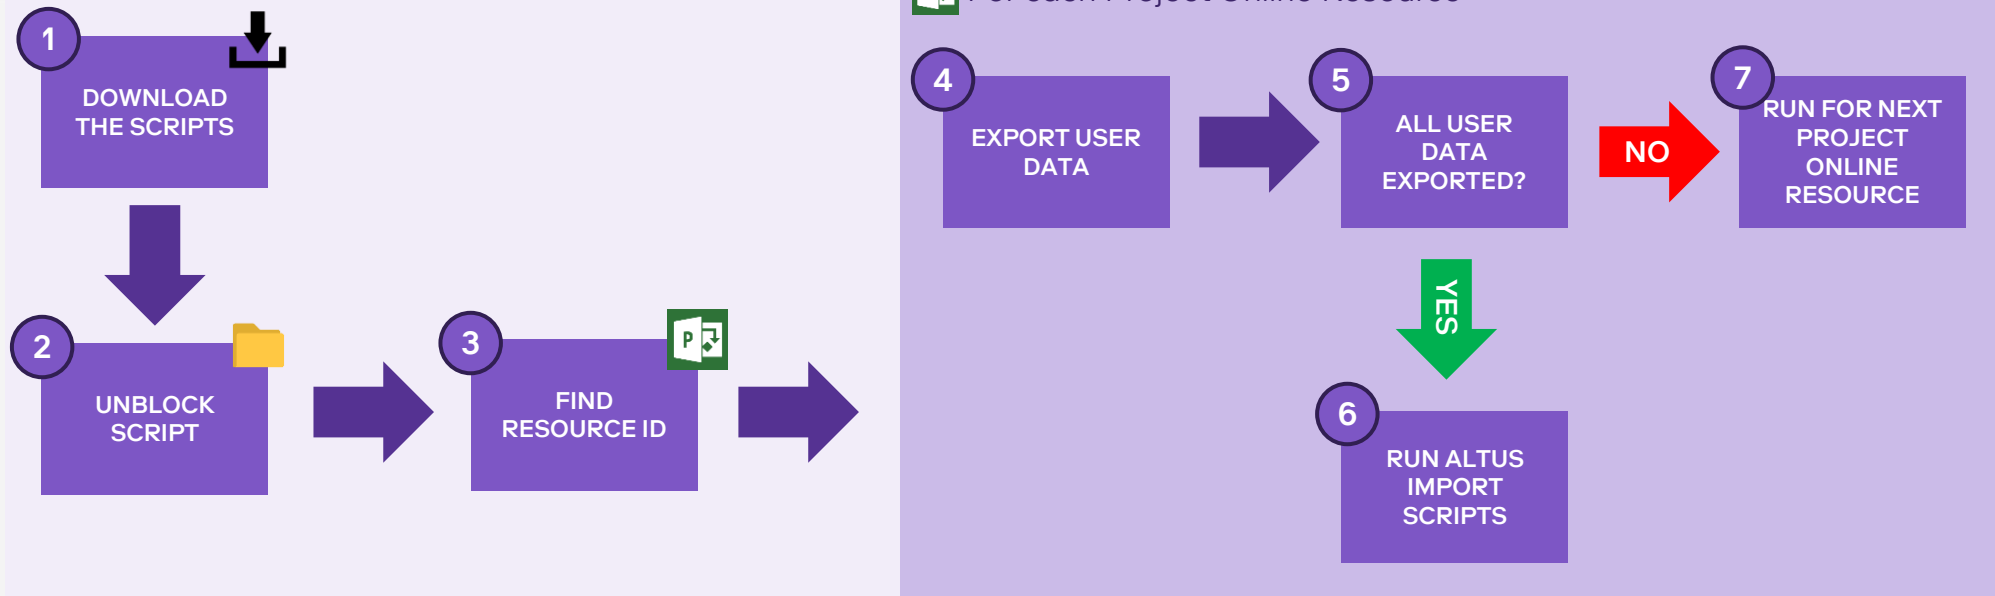

</> Altus Script | .MPP file extract

Creation of .MPP files for project schedules stored in Project Online.

.MPP extraction from Project Online



</> Microsoft Script | .MPP file extract


Creation of .MPP files for project schedules stored in Project Online.

#	Step	Details
1	Download the scripts	Export user data from Project Online Download Scripts
2	Unblock the scripts	Export user data from Project Online Unblock your files
3	Find Resource IDs	Export user data from Project Online Find Resource IDs
4	Export user data	Export user data from Project Online Export User Data
5	All user data exported?	The Microsoft script is user specific and will need to be updated for each resource in Project Online.
6	Run Altus import scripts	Once you have exported all Project Online data, you can then proceed to running the Altus scripts.
7	Run for next Project Online resource	Export user data from Project Online Export User Data


</> Altus Script | Resource Import

Creation of bookable resources in Altus.

Resource Import process.

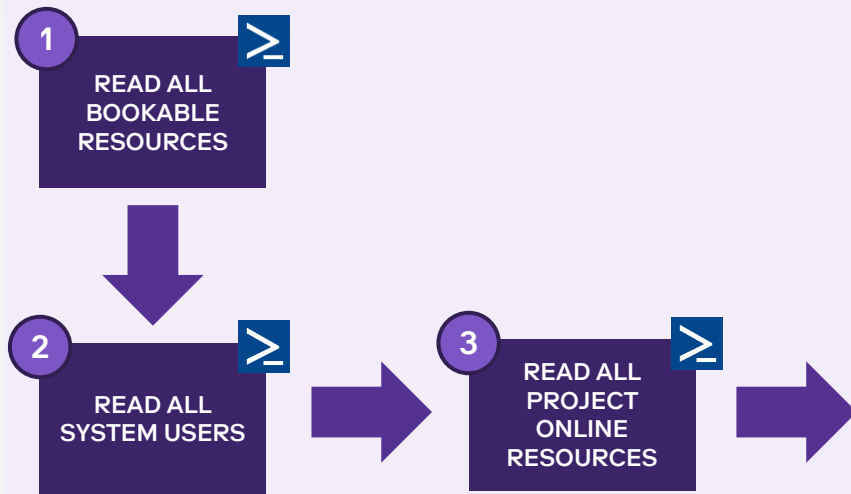

[Product Backlog Item 37574 POL Migration \(1B\): Create Reusable PowerShell Script to Migrate Projects from Project Online to Altus \(Dataverse\)](#)

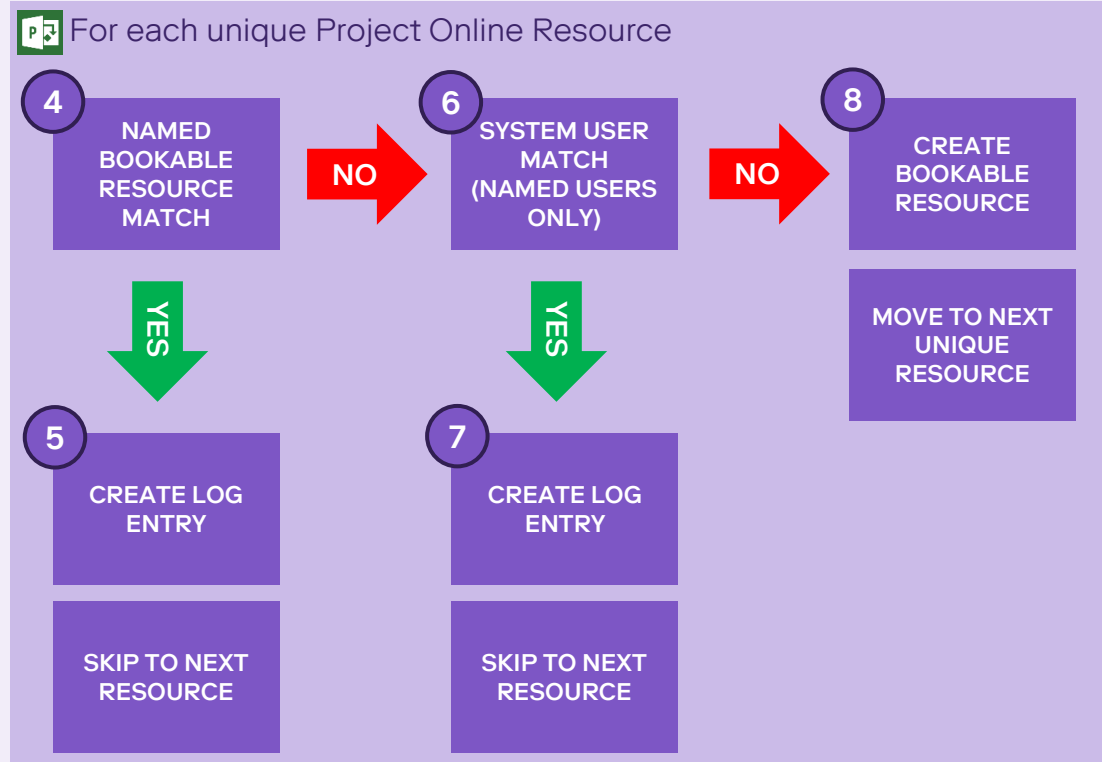

</> Altus Script | Resource Import

Creation of bookable resources in Altus.

#	Step	Details
1	Read all bookable resources	The script will return a list of all bookable resources that existing the in the target Altus environment.
2	Read all system users	The script will return a list of all system users that existing the in the target Altus environment.
3	Read all Project Online resources	The script will return a list of resources from the project schedule.
4	Named bookable resource match?	Does the resource in the project schedule match an existing bookable resource in Altus?
5	Create log entry, move to next resource	If there is a match, do not create a new bookable resource and move to the next project schedule resource.
6	System user match?	Does the resource in the project schedule match an existing system user in Altus?
7	Create log entry, move to next resource	If there is a match, do not create a new system user and move to the next project schedule resource.
8	Create bookable resources, move to next	If there is no match between the project schedule and Altus, a new bookable resource will be created.

</> Altus Script | Resource Import


Which fields in the Altus bookable resource table will be updated.

Bookable Resources Data Created		
Field	Type	Example Data
Name	Single line of text	Albert Connell
User	Lookup	Albert Connell
Target Utilisation	Whole number	100
Primary Role	Lookup	Unclassified (Generic)
Enterprise Calendar	Lookup	Default Calendar


</> Altus Script | Project Import

Creation of Projects in Altus.

Project Import process.

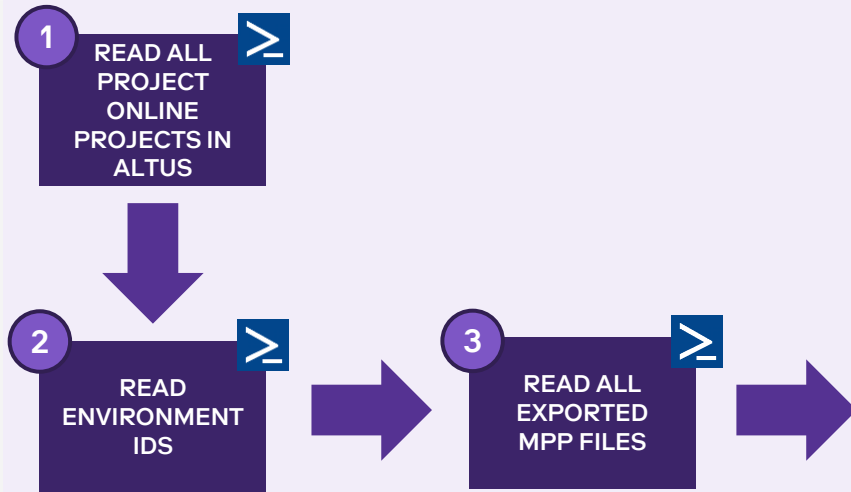

[Product Backlog Item 37574 POL Migration \(1B\): Create Reusable PowerShell Script to Migrate Projects from Project Online to Altus \(Dataverse\)](#)

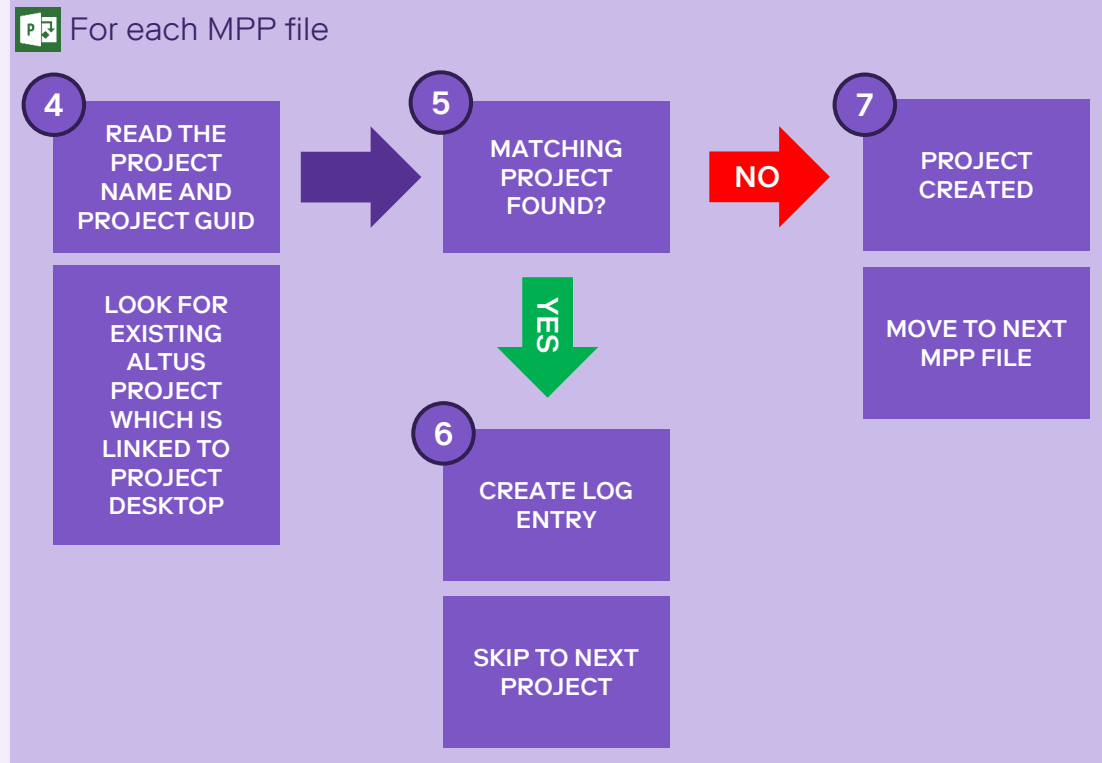

</> Altus Script | Project Import

Creation of Projects in Altus.

#	Step	Details
1	Read all project online connected schedules in Altus	The script reads all projects in the Altus environment which have an external execution type set to Project Online.
2	Read Environment IDs	Environment IDs are captured to ensure that the schedules are published to the correct Altus instance.
3	Read all exported .MPP files	The script will then get the names all schedules exported by the Microsoft script.
4	Read Project Name and GUID	The name and GUID from Altus are read for matching purposes.
5	Matching project found?	The script will match between the .MPP name and the Altus project name.
6	Create log entry, move to next project	If a match is found, a new project won't be created, and the script will move to the next .MPP file in the folder.
7	Create project, move to next .MPP file	If no match is found, a new project will be created, and the script will move to the next .MPP file in the folder.


</> Script | Project Import

Which fields in the Altus Projects table will be updated.

Projects Data Created		
Field	Type	Example Data
Name	Single line of text	AA Tenant Renewal R300
Project Type	Lookup	Major Project
External Project Id	Single line of text	38cf727e-ca29-4b80-8192-5f0195e92889

</> Altus Script | Schedule Publish

Publish project schedule data to Altus.

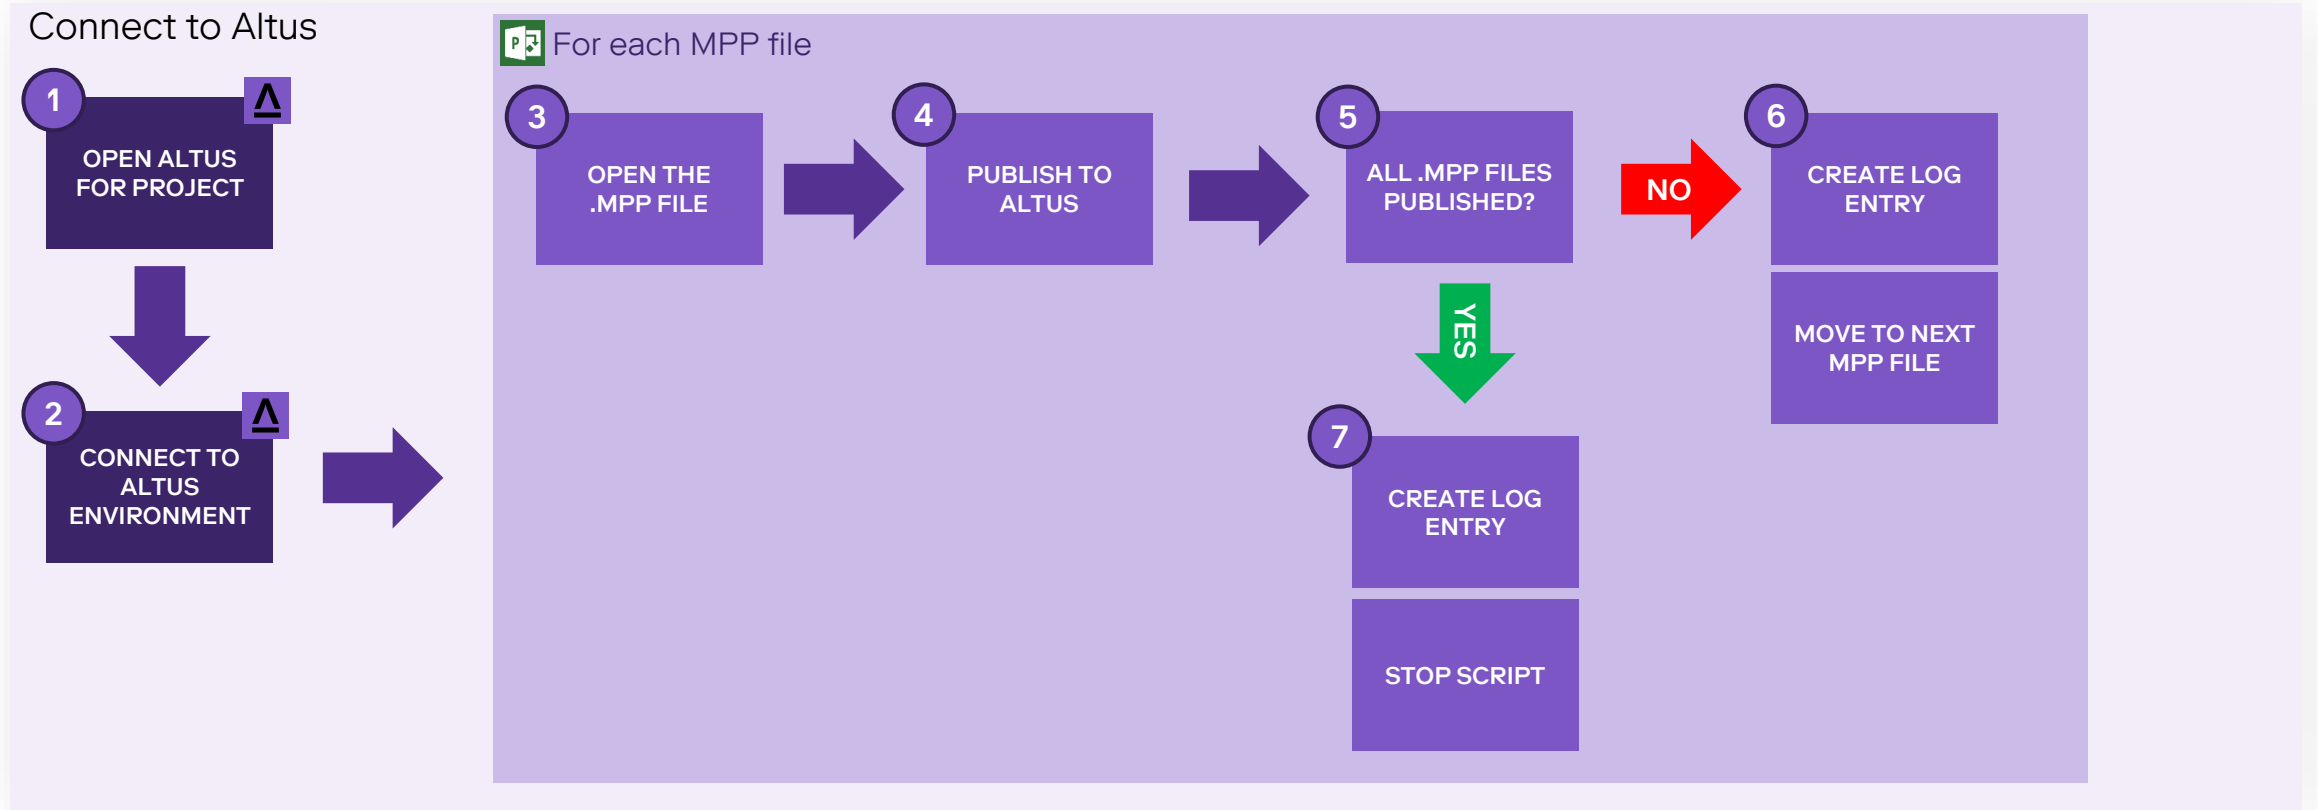

</> Altus Script | Schedule Publish

Publish project schedule data to Altus.

#	Step	Details
1	Open Altus for Project	The first step is to open Altus for Project – the schedule publish process requires this desktop application.
2	Connect to Altus environment	Once done, a connection needs to be made to the target Altus environment.
3	Open the .MPP file	When the connection has been established, the script will open every .MPP in the specified folder.
4	Publish to Altus	The script will publish each schedule, then will close and move to the next .MPP file.
5	All .MPP files published?	The script will check after each .MPP publish for the next file.
6	Move to next .MPP file	If there are more files to publish, the script will continue on and create log entries.
7	Stop Script	Once all .MPP files in the folder have been published, the script will stop and create the final log entry.




Data Migration Project Online data

Project Online data

What data do Customers need to get from Project Online?


Projects & Resources will need to be extracted from Project Online.

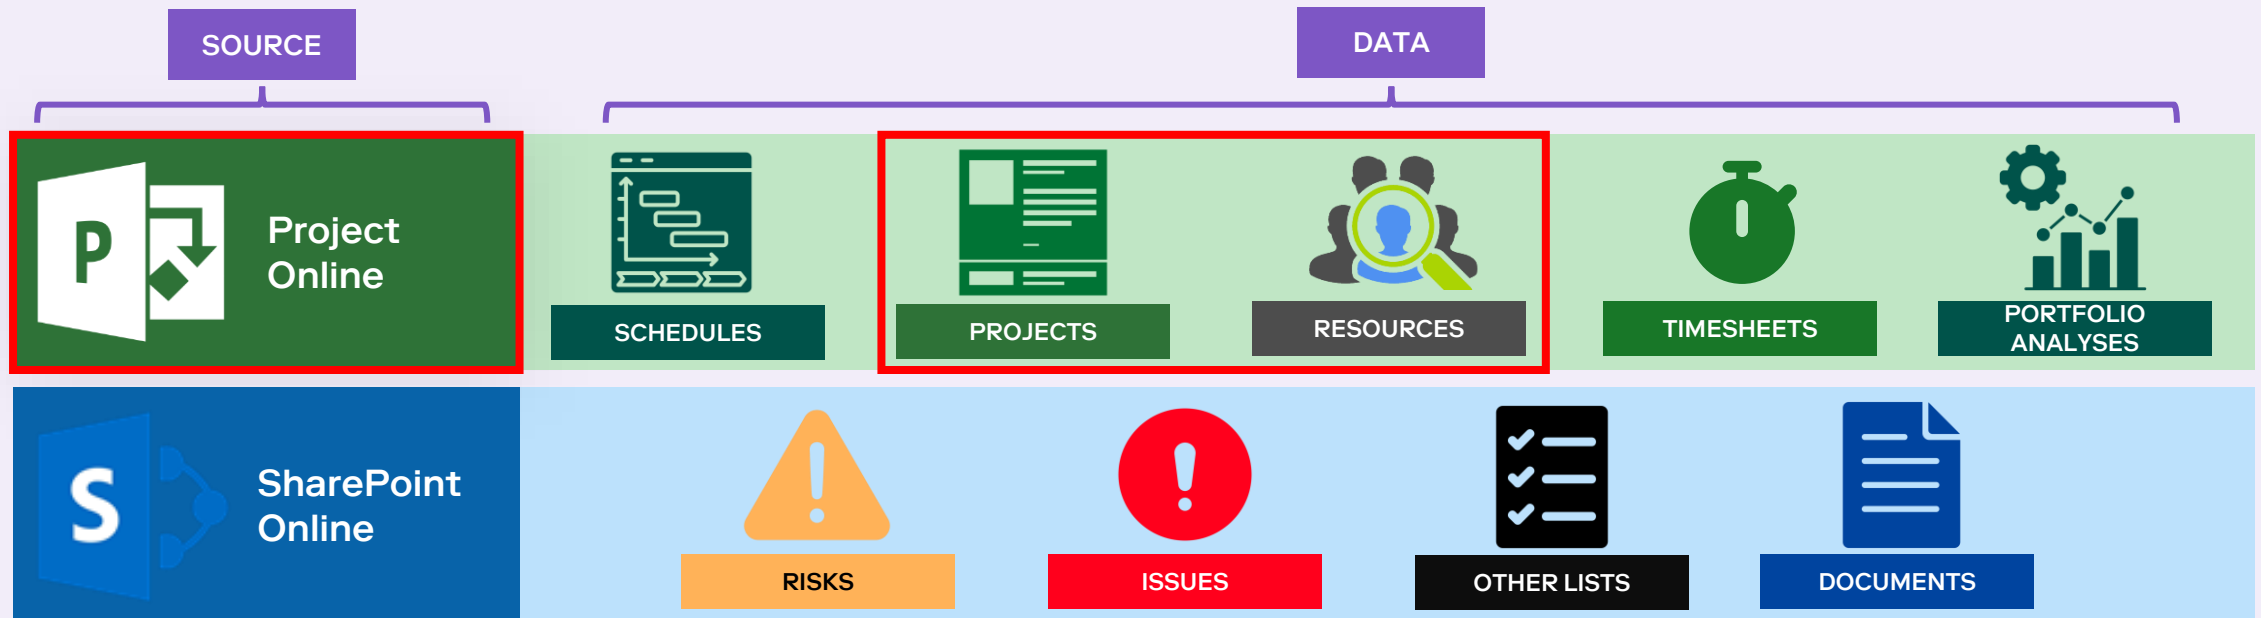

►► Project Online Data Migration | Approach

How can Customers get the rest of their data from Project Online into Altus?

The diagram below outlines the high-level process for migrating remaining Project Online data.

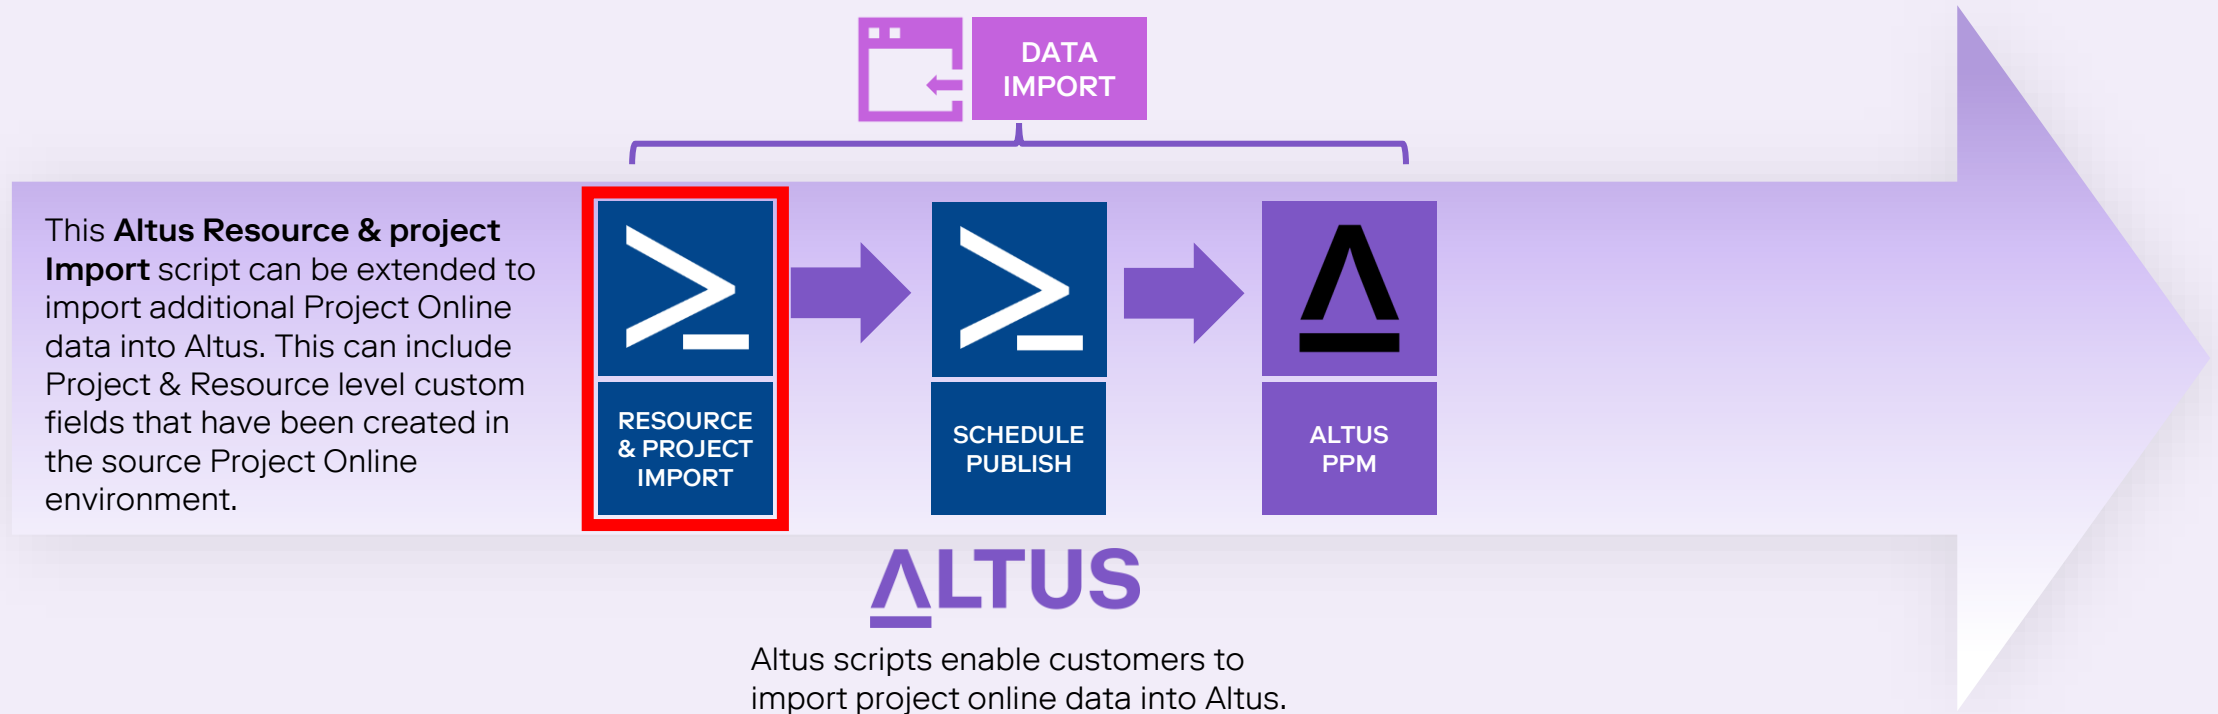

</> Script | Project Import

This part of the project import script can be extended to include additional fields.

```
# Create Project record in Dataverse
if ($ExecutionMode) {
    if ($null -eq $orphanedProject) {
        Write-Host "Creating Project record in Dataverse for $projectName..." -ForegroundColor Green
        $project = @{
            'sensei_name' = $projectName
            'sensei_projecttype@odata.bind' = "/sensei_enterpriseprojecttypes($($DefaultProjectTypeId))"
            'sensei_externalprojectid' = "ProjectDesktop_$projectGuid"
        }
        $newProjectId = New-Record -setName 'sensei_projects' -body $project
        $nProjectsCreated++
        Write-Host "Created Project record in Dataverse for $projectName with ID: $newProjectId" -ForegroundColor Green
    }
}
```

</> Script | Resource Import

This part of the resource import script can be extended to include additional fields.

```
# Create a new Bookable Resource in Dataverse and log the creation
```

```
    Write-Host "Creating Bookable Resource for '$($projectResource.ResourceName)' with login '$($projectResource.ExtractedEmail)'." -  
ForegroundColor Green
```

```
# Create new Bookable Resource
```

```
$newBookableResource = @{
```

```
    'sensei_name' = $projectResource.ResourceName
```

```
    'sensei_resourcetype' = 955000001 # Named Resource
```

```
    'sensei_user@odata.bind' = "/systemusers($($matchingSystemUser.systemuserid))"
```

```
    'sensei_targetutilization' = $DefaultTargetUtilisation
```

```
    'sensei_primaryrole@odata.bind' = "/sensei_bookableresources($($DefaultPrimaryRoleId))"
```

```
    'sensei_enterprisecalendar@odata.bind' = "/sensei_enterprisecalendars($($DefaultEnterpriseCalendarId))"
```

```
}
```

</> Script | PowerShell Patterns

What patterns can be used to migrate Project and Resource data from Project Online to Altus?

Field Type	PowerShell Script Pattern / Example
Single line of text	
Multiple lines of text	
Cost	
Date	
Duration	
Flag	
Number	
Calculated	N/A These fields need to be created in Altus once the migration of other data has been completed.

</> Migrating Lookup Table values

The approach for migrating Lookup tables is slightly different.

Need the Altus Development team to confirm the approach here.




Data Migration Timesheets

Timesheets

What data do Customers need to get from Project Online?

The approach for timesheets is covered off in the next slide.



▶▶ Timesheets | Approach

What approach is Altus taking with the migration of timesheets, specifically Actuals?

Altus has a schedule agnostic position where we enable customers to connect to a wide variety of scheduling tools. To ensure this works consistently, we have architected Altus to be the master system for actuals, notably when timesheets actuals are processed back to the connected schedule.


The Altus approach is to ensure that Project Desktop actuals are not overwritten when approved Altus timesheets are imported. As such, we have devised an approach using a date to honour 'protected actuals' that will work in the following scenarios.

Actuals Management Method	Details
Continue managing actuals in .MPP	Partner or Customer won't be using timesheets in Altus for migrated schedules and will continue to update actuals in the .MPP file.
Start using timesheets in Altus	Partner or Customer plans to start using timesheets in Altus once .MPP files have been migrated.
Project Online Timesheet Migration plus Altus Timesheets	Partner or Customer plans to migrate all historical Project Online timesheets into Altus.
Migrate to Altus and disconnect .MPP file	Partner or Customer plans to migrate projects via MPP files and then disconnect them to utilise the Altus native scheduler. Note: This method will cause a loss of actuals in the Altus if timesheets are imported, but the disconnected MPP actuals are unaffected.

▶▶ Timesheets | 'Protect Actuals Before' Date

How are we protecting actuals in the .MPP to avoid these from being overwritten by Altus Timesheets?


- To ensure that actuals in the .MPP schedule file are not overwritten, we have implemented logic to prevent this from occurring.
- This is achieved using an assignment-level date field referred to as **Protected Actuals Before**.
- This is the date when approved Altus timesheets actuals are first imported to the .MPP file.
- This ensures that existing historical actuals are protected and not overwritten when approved timesheets actuals are imported to the .MPP file.
- Note, this date is set at the assignment-level rather than the task-level. This ensures that actuals are protected at the appropriate level and cater for timesheet actuals being processed by different resources at different dates.
- This date enables Partners and Customers to avoid migrating timesheets as this date will preserve historical actuals in the MPP.

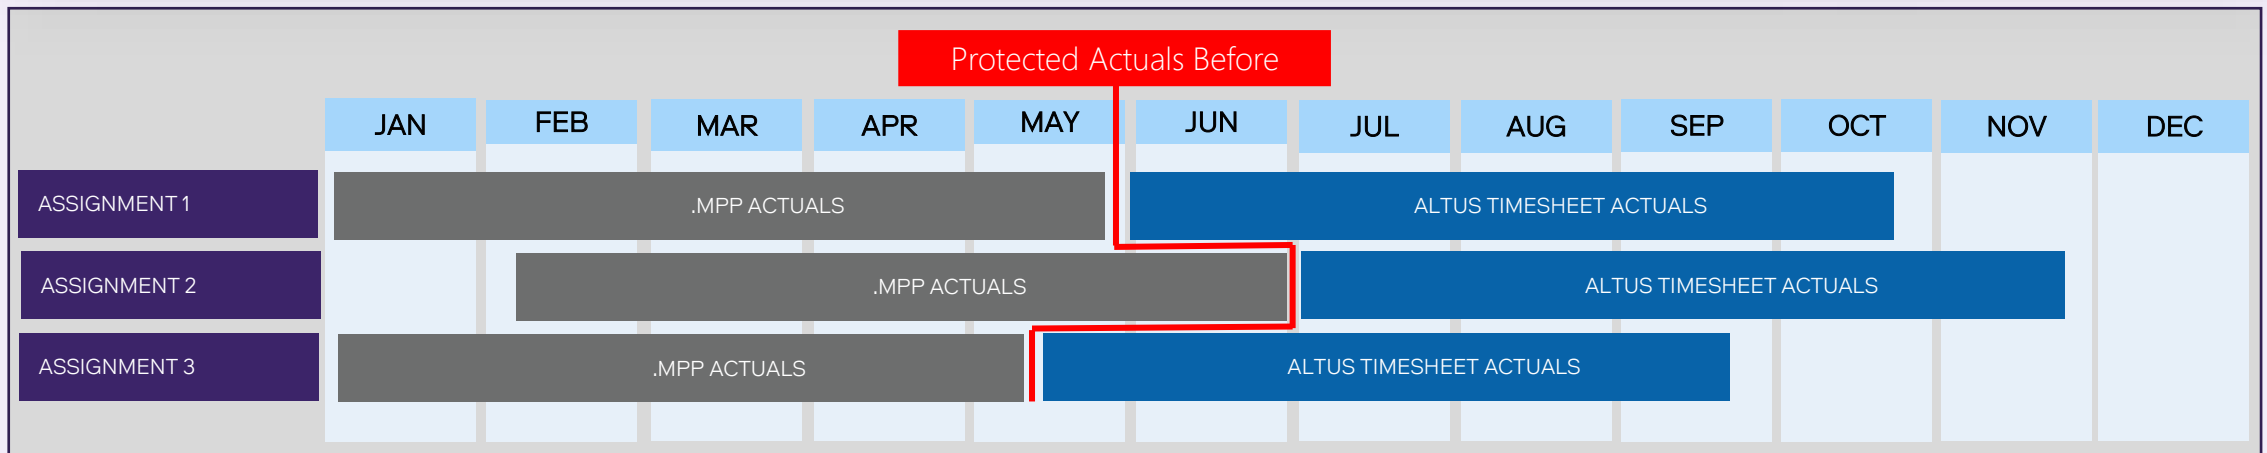

► Timesheets | 'Protect Actuals Before' Date

How are we protecting actuals in the .MPP to avoid these from being overwritten by Altus Timesheets?

- To ensure that actuals in the .MPP schedule file are not overwritten, we have implemented logic to prevent this from occurring.
- This is achieved using an assignment-level date field referred to as **Protected Actuals Before**.
- This is the date when approved Altus timesheets actuals are first imported to the .MPP file.
- This ensures that existing historical actuals are protected and not overwritten when approved timesheets actuals are imported to the .MPP file.
- Note, this date is set at the assignment-level rather than the task-level. This ensures that actuals are protected at the appropriate level and cater for timesheet actuals being processed by different resources at different dates.
- This date enables Partners and Customers to avoid migrating timesheets as this date will preserve historical actuals in the MPP.

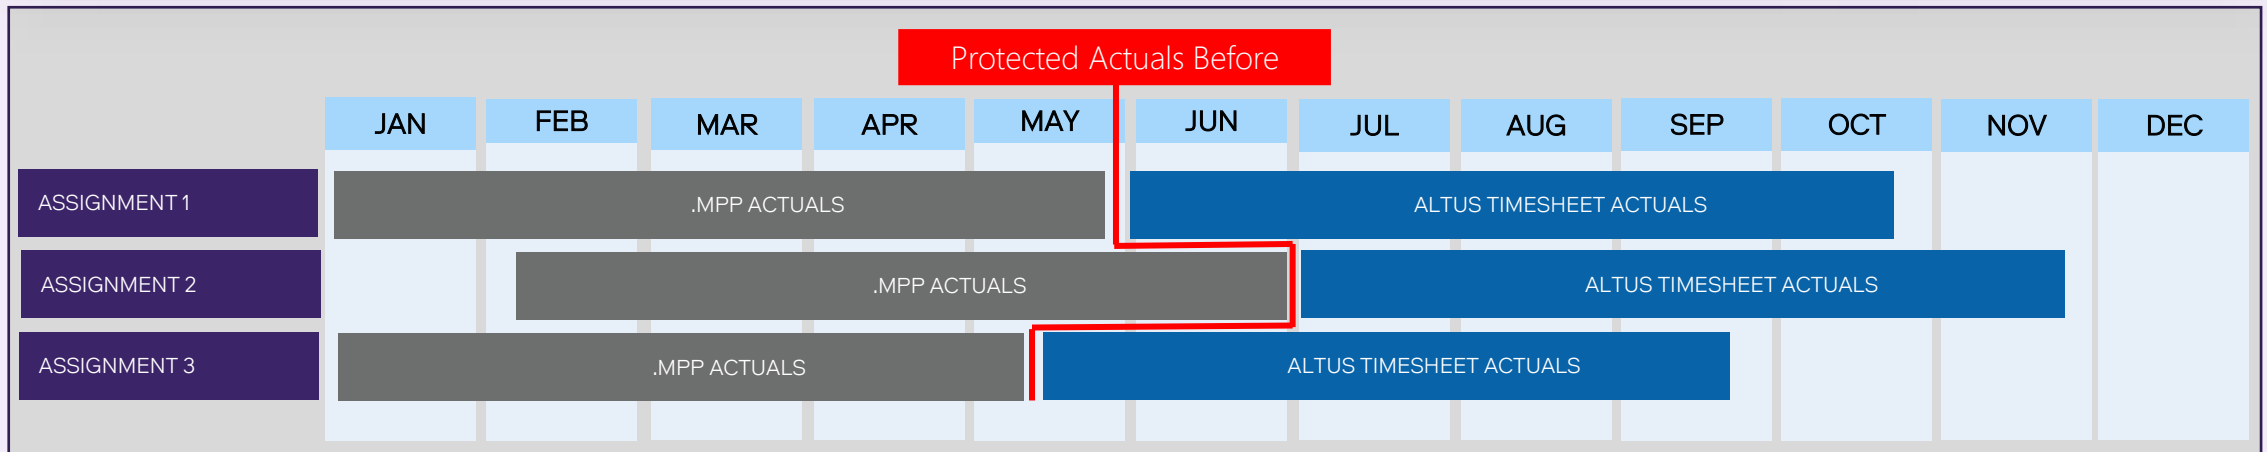

▶▶ Timesheets | Actuals Import Scenarios

What approach is Altus taking with the migration of timesheets, specifically Actuals?

The table below provide details about the various scenarios that customers can use to update actuals in their project schedules.

Resource Type	Actuals Method	Details
Generic, Cost, & Material	% Complete	These actuals are not updated by Actuals timesheet imports.
Altus Bookable Resource	% Complete	
	Timesheets	Importing timesheets into the .MPP file will update matching assignments. The Protected Actuals Before date will prevent historical actuals from being overwritten by Altus.




Data Migration Portfolio Analyses

Portfolio Analyses data


What data do Customers need to get from Project Online?

Projects & Resources will need to be extracted from Project Online.

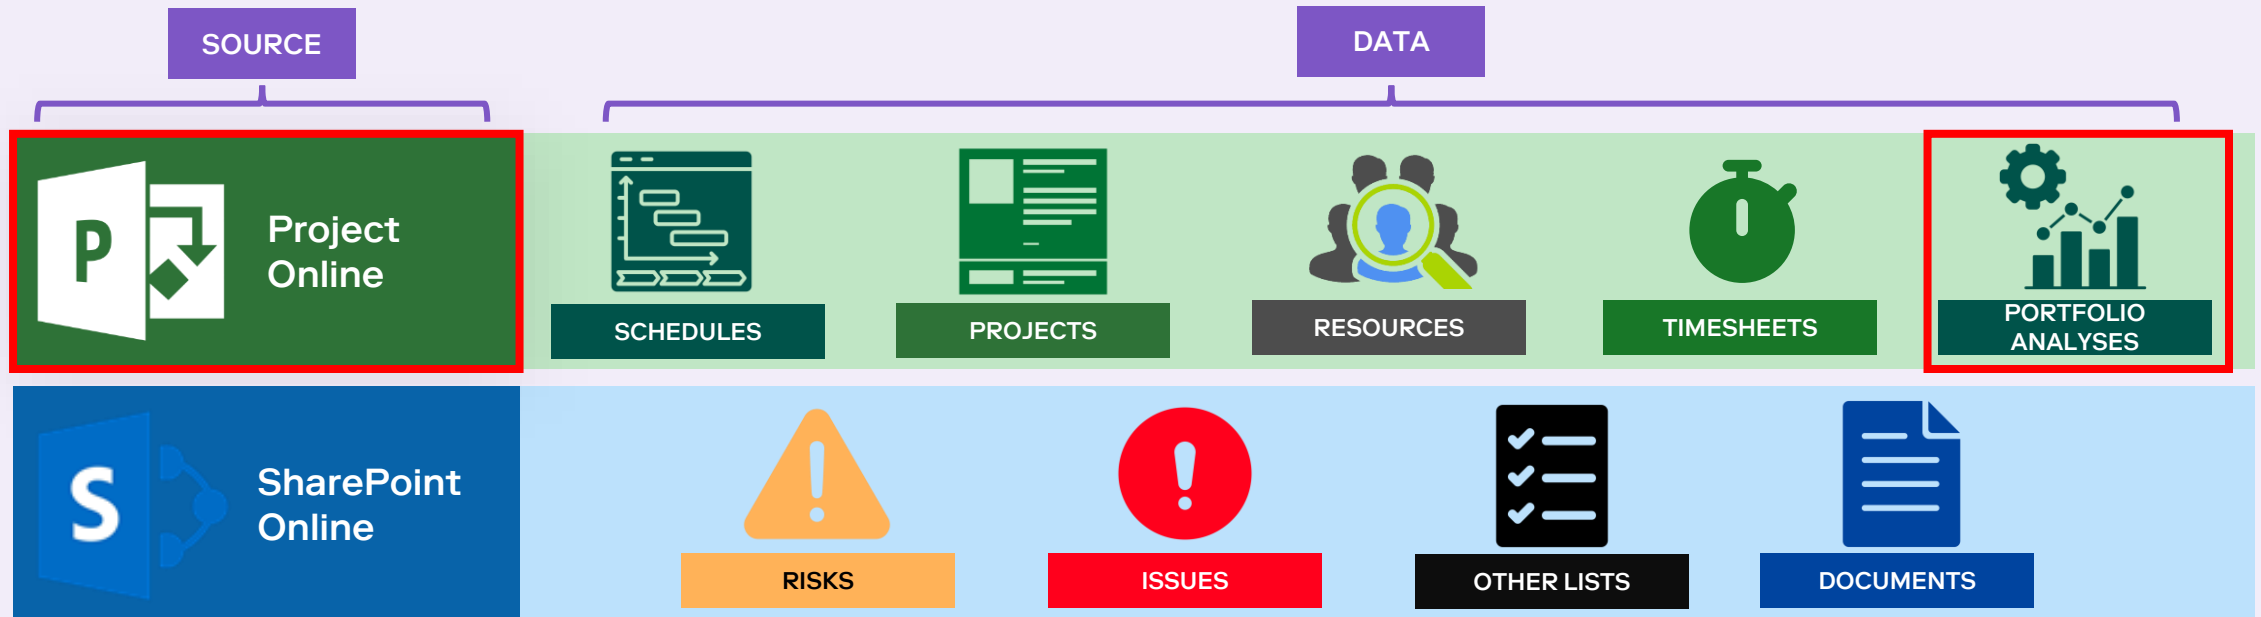

►► Portfolio Analyses Data | Approach


The diagram below outlines the method for migrating Portfolio Analyser data into Altus.

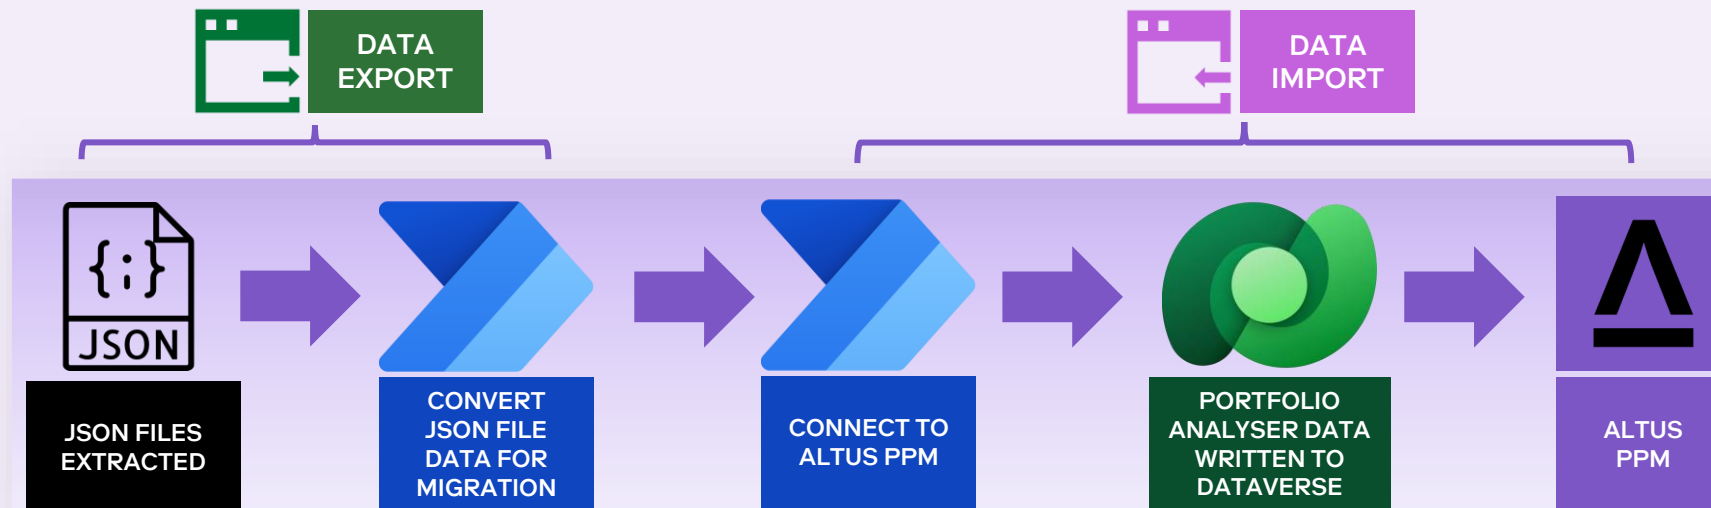

This method will write the Portfolio Analyser data (Business Drivers and Portfolio Scenarios) to the relevant Dataverse tables in Altus.

</> Portfolio Analyses Data | Approach


The diagram below outlines the method for migrating Portfolio Analyser data into Altus.

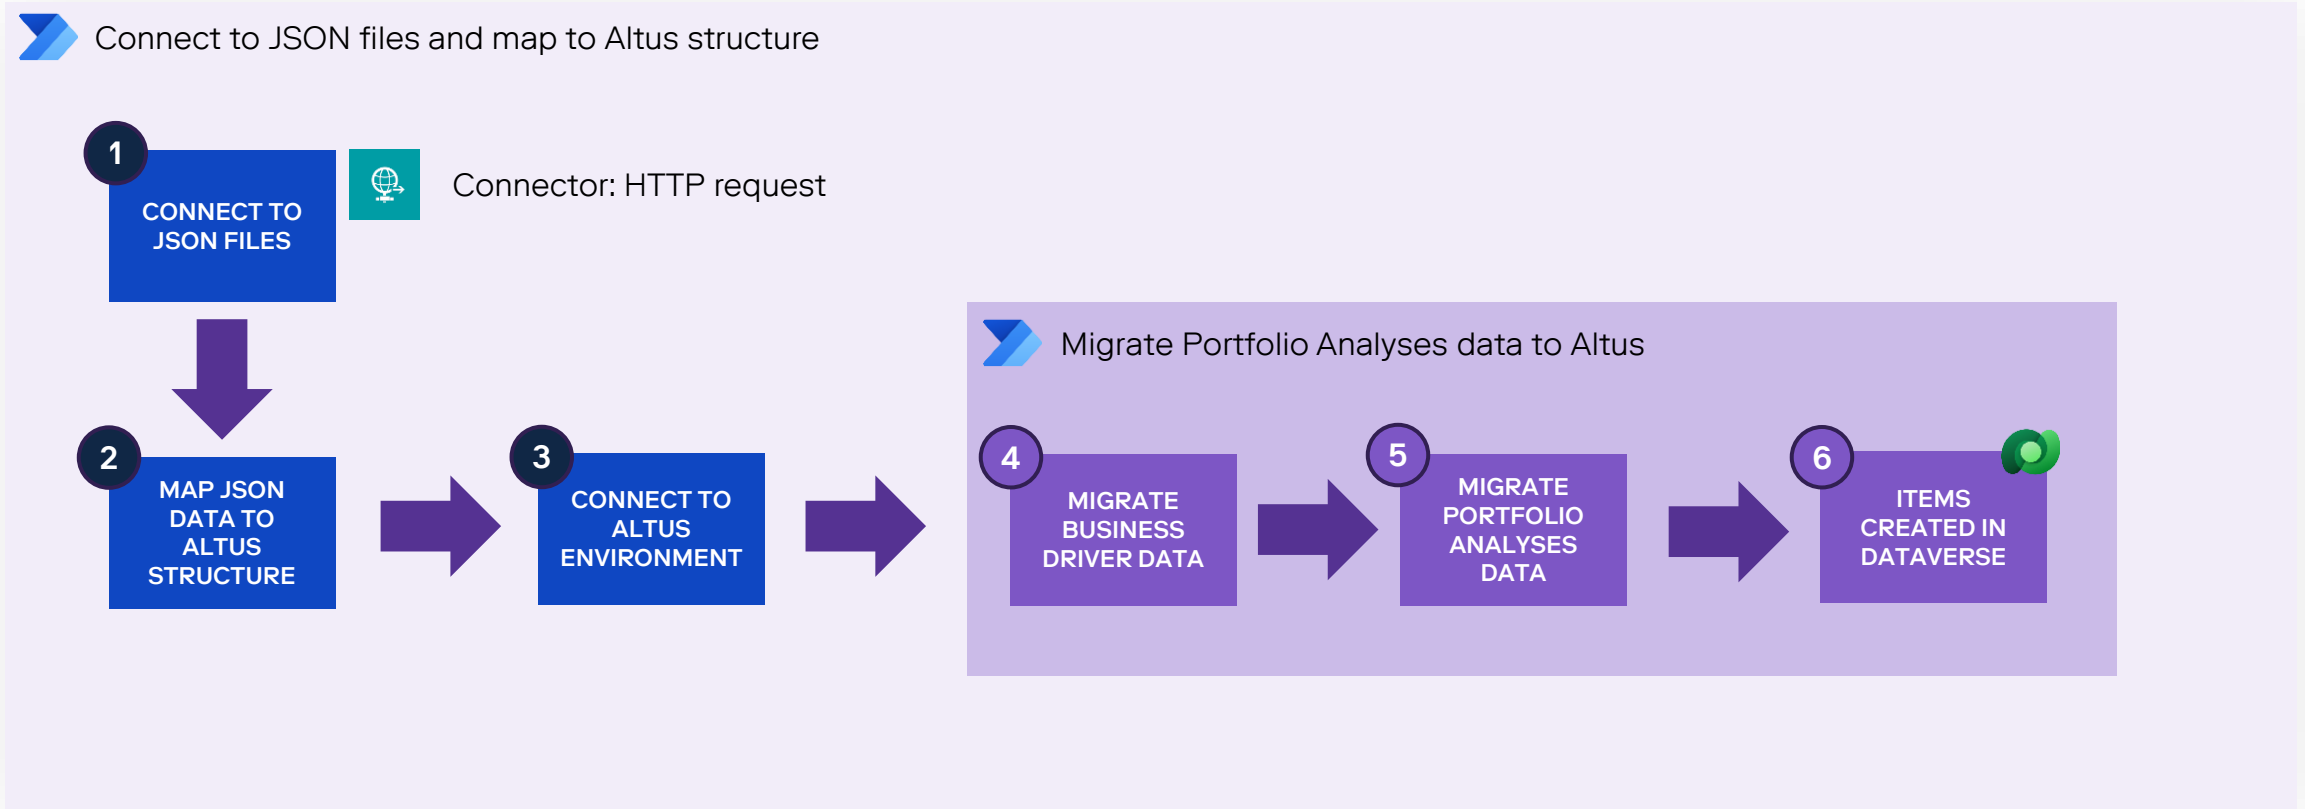

</> Portfolio Analysis Data | Approach

Migration of portfolio analysis data, including business drivers.

#	Step	Details
1	Connect to JSON files	The Power Automate flow will connect to the Business Drivers and Portfolio Analyses JSON files.
2	Map JSON data to Altus Structure	It will then map the fields to the corresponding fields in Altus.
3	Connect to Altus Environment	Then it will connect to the target Altus environment where the data is to be migrated to.
4	Migrate Business Driver Data	The first step will involve migrating in the Business Drivers.
5	Migrate Portfolio Analyses Data	Once this has been completed, the remaining Portfolio Analyses data will be migrated in.
6	Items created in Dataverse	This data will be written directly to the relevant Dataverse tables.

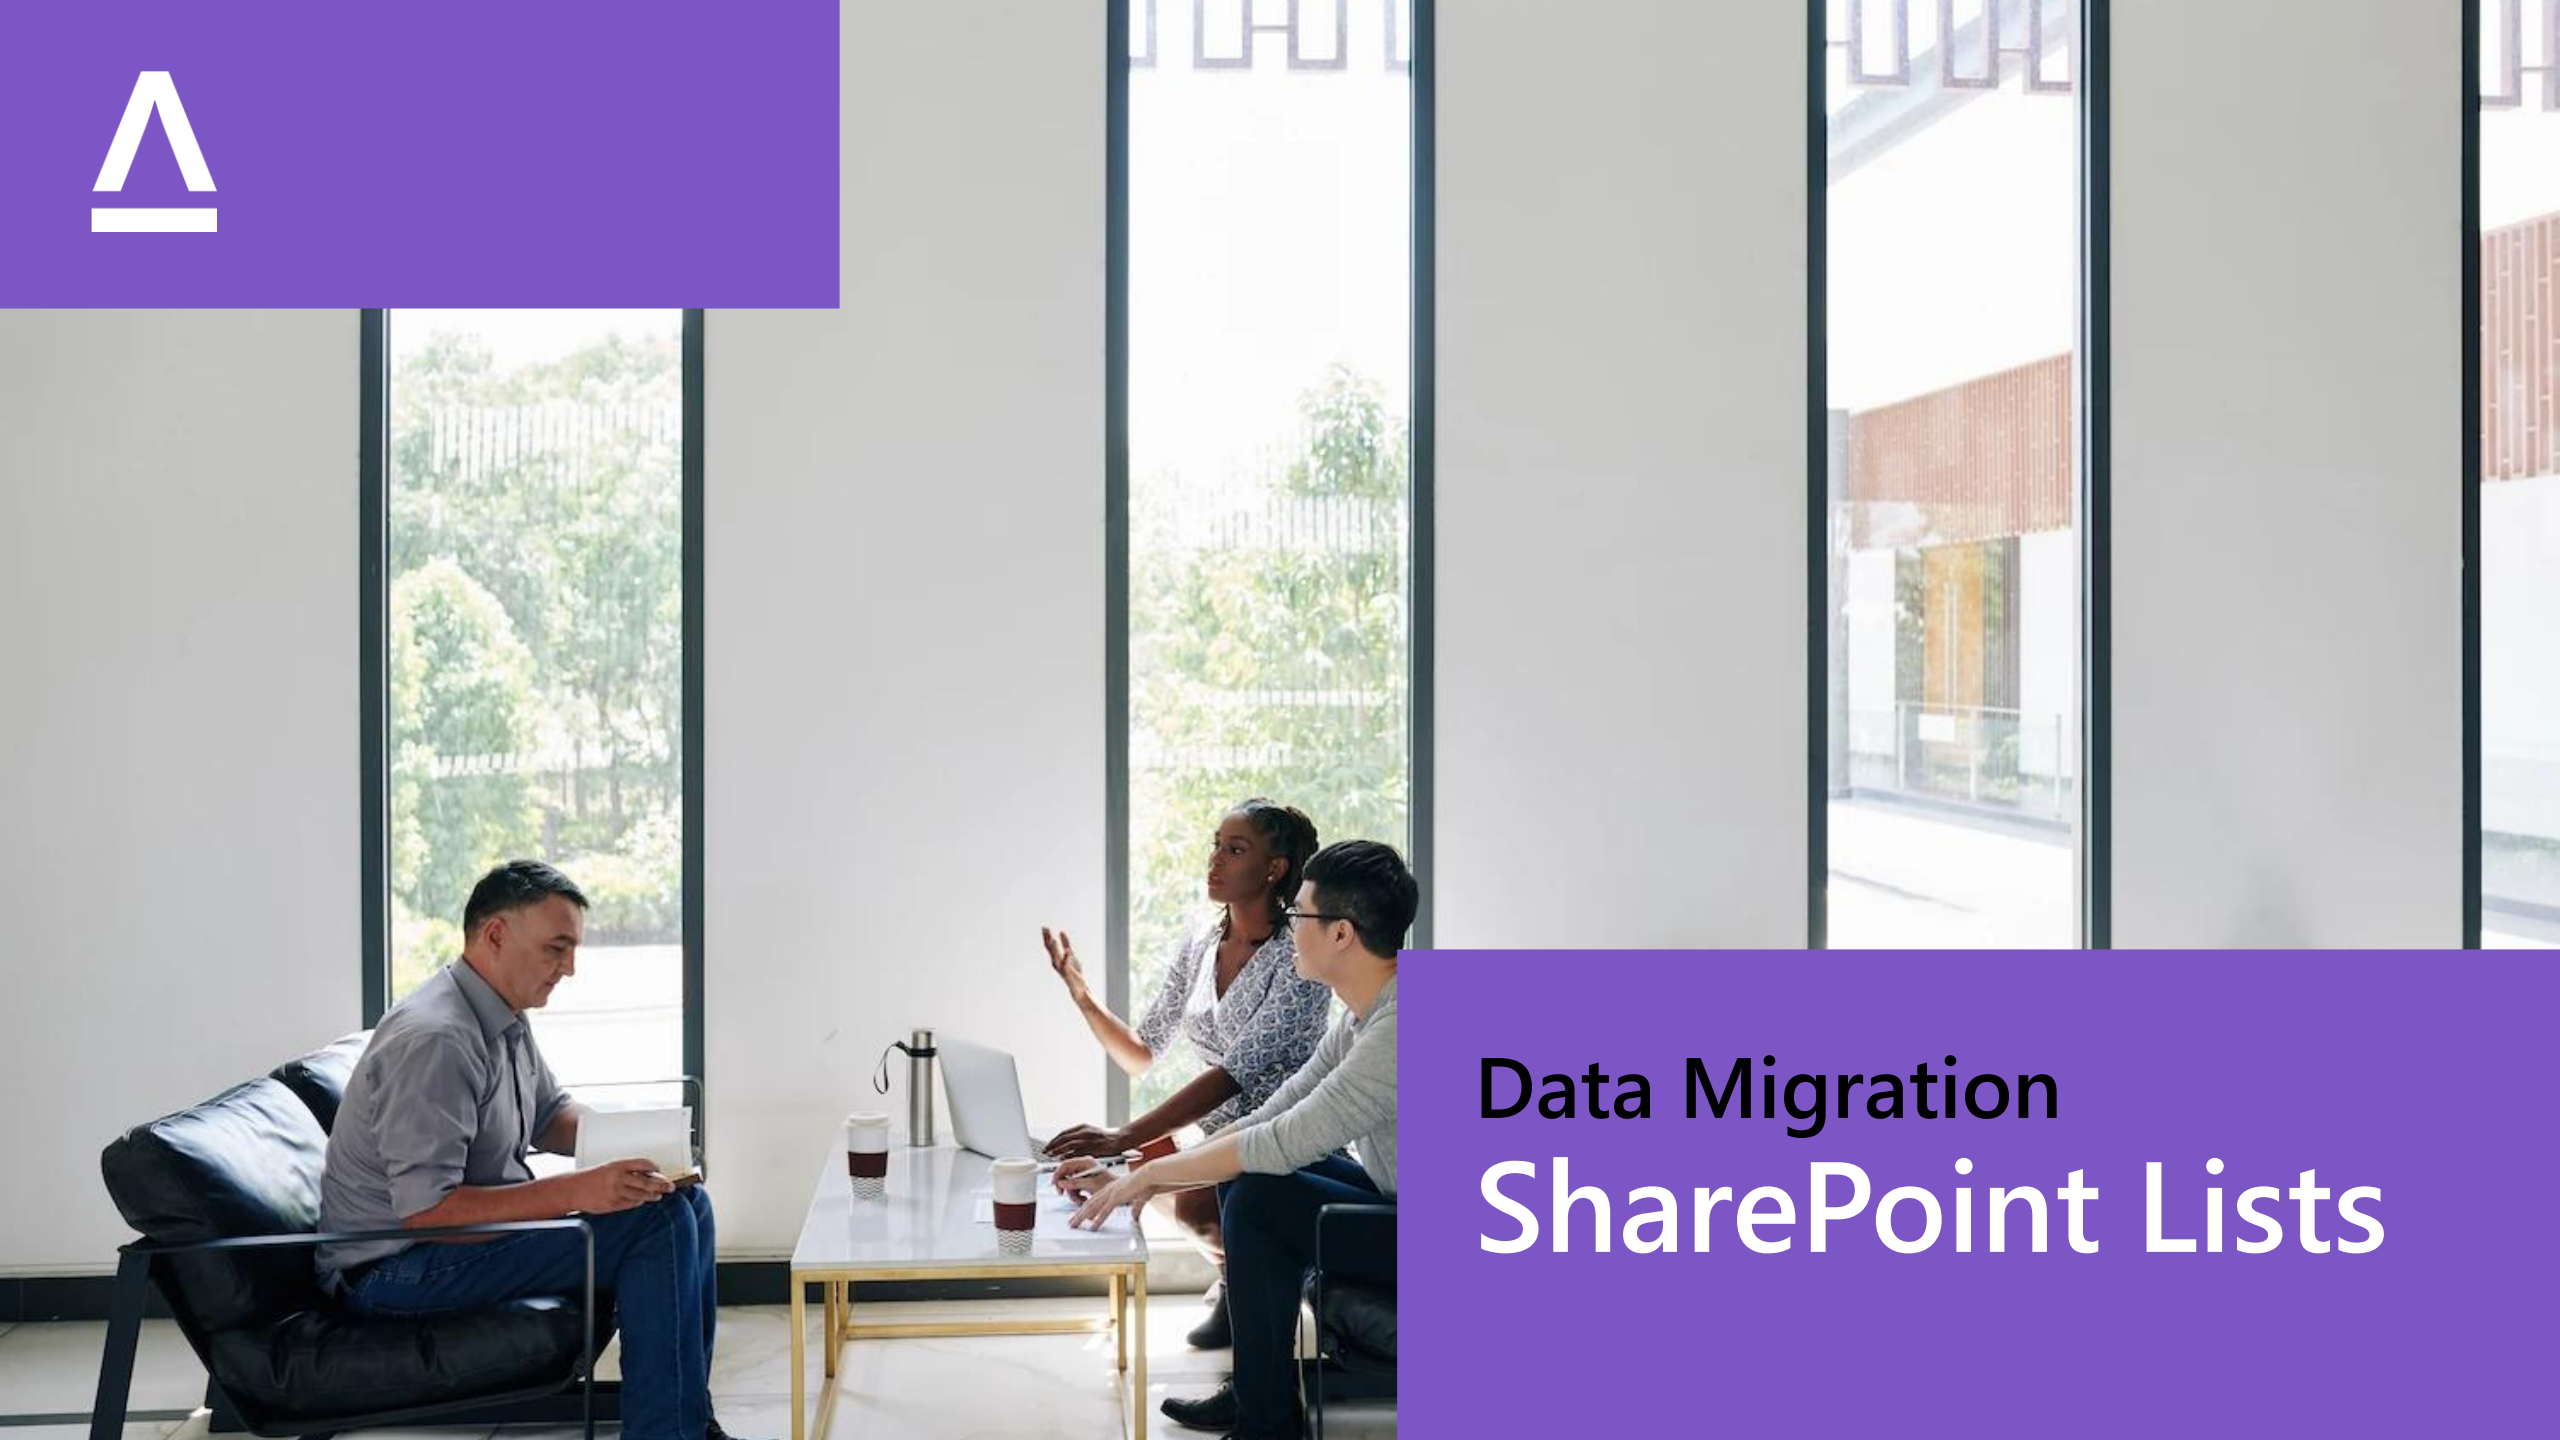


Data Migration SharePoint Lists

SharePoint Lists

What data do Customers need to get from SharePoint Online?

List data (such as Risks and Issues) will need to be extracted from SharePoint Online.



►► SharePoint Lists | Approach

The diagram below outlines the method for migrating list-based data into Altus.



The approach above is designed to work with the OOTB registers in Altus.
Any custom registers that have been created in SharePoint Online will need to be configured in Altus prior to the migration.

►► SharePoint Lists | Approach

The diagram below outlines the method for migrating list-based data into Altus.



The approach above is designed to work with the OOTB registers in Altus. Any custom registers that have been created in SharePoint Online will need to be configured in Altus prior to the migration.

</> SharePoint Lists | Approach

Migration of list-based data

#	Step	Details
1	Connect to SharePoint Online	The first Power Automate flow will connect to the source SharePoint Online environment.
2	Retrieve Sub-Sites and Lists	Once connected, it will retrieve all sub-sites and the lists within these sub-sites.
3	Trigger for a Single Project	The migration script is triggered for a single project.
4	Retrieve List Items	The script will retrieve the list items for the selected project.
5	Connect to Altus	Then it will connect to the target project in Altus.
6	Create Items in Dataverse	The list items will be created as new records in the relevant Dataverse table.




Data Migration SharePoint Documents

SharePoint Documents | Overview

What data do Customers need to get from SharePoint Online?

Documents and their associated metadata will need to be extracted from SharePoint Online.

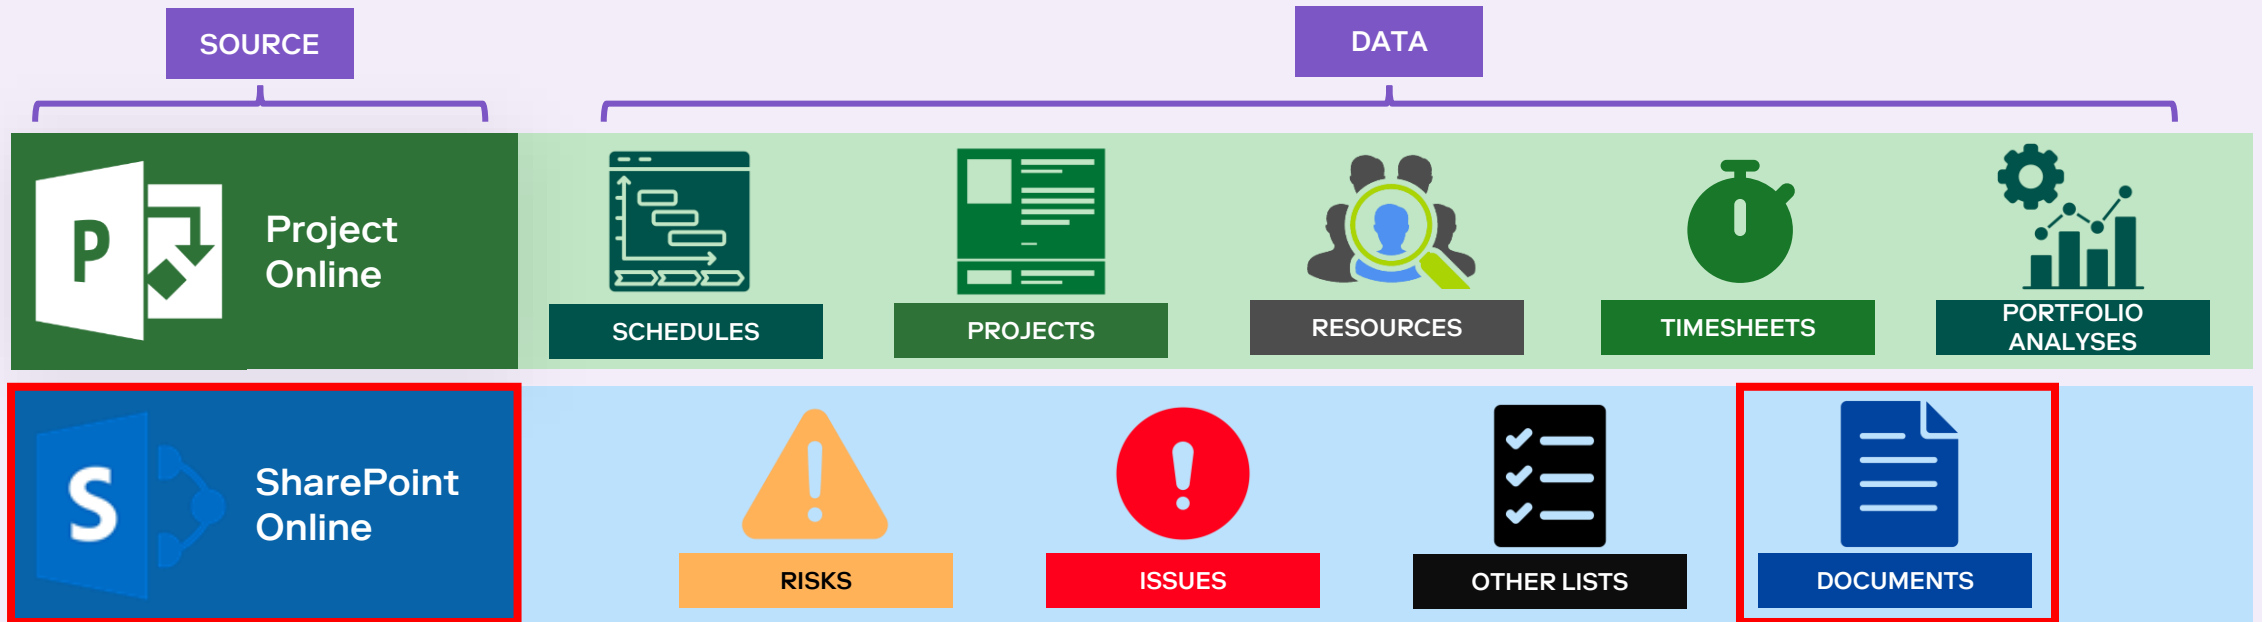

► SharePoint Documents | Options

What options are the for migrating SharePoint documents?

At Altus, we have identified three possible options for migrating SharePoint Documents. The chosen approach will depend on customer requirements, time available, and the costs involved. The table below provides a summary of the three approaches.

#	Option	Details
1	Move SharePoint Site Collection out of Project Online	This approach involves moving all the sub-sites out of the Project Online site collection. This will provide the Partner or Customer more time to migrate these documents later.
2	Power Automate document migration to O365 Groups	This approach leverages Power Automate to move documents from the SharePoint document library to the Office Group document library. This is triggered on a per project basis.
3	Share Gate Document Migration.	This approach involves purchasing Share Gate and using this to complete a document migration from the SharePoint document library to the Office Group document library

► SharePoint Documents | Options

What options are the for migrating SharePoint documents?


At Altus, we have identified three possible options for migrating SharePoint Documents. The chosen approach will depend on customer requirements, time available, and the costs involved. The table below provides a summary of the three approaches.

#	Option	Cost	Storage	Metadata	Version History	Altus Teams Integration	Complexity	Comprehensive
1	Cross-Tenant SharePoint Migration	\$15 USD Per User					Low	Moderate
2	Power Automate Document Migration	\$Nil					Medium	Moderate
3	Share Gate Document Migration.	From \$5,995 USD					High	Full

</> SharePoint Lists | Approach

The diagram explains in more detail how the migration approach will migrate the list-data.

 Connect to SharePoint and retrieve projects and lists

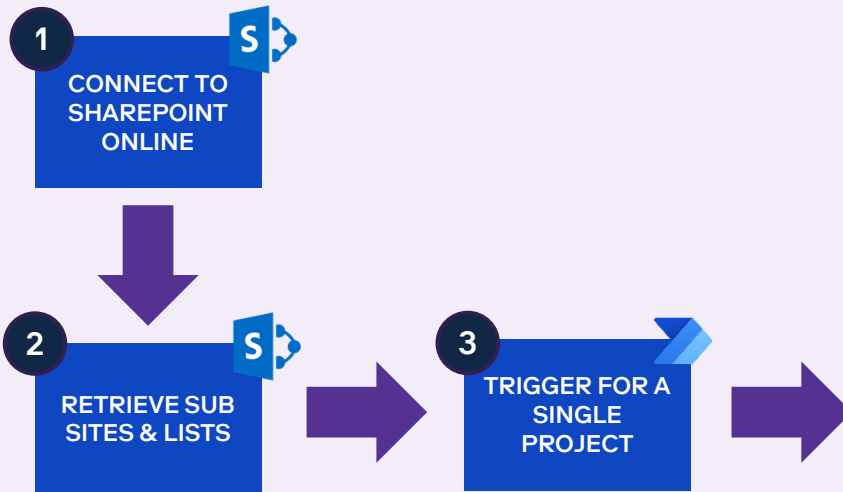

This migration approach is designed to be run on a per-project basis and will copy the list items into the relevant Dataverse table and link them to the relevant project. This will enable Partners and Customers to determine how best to run these scripts without committing to a 'big bang' approach.

 Migrate items for a single project



► SharePoint Documents | Options

What options are the for migrating SharePoint documents?

At Altus, we have identified three possible options for migrating SharePoint Documents. The chosen approach will depend on customer requirements, time available, and the costs involved. The table below provides a summary of the three approaches.

#	Option	Cost	Storage	Metadata	Version History	Altus Teams Integration	Complexity	Comprehensive
1	Cross-Tenant SharePoint Migration	\$15 USD Per User					Low	Moderate
2	Power Automate Document Migration	\$Nil					Medium	Moderate
3	Share Gate Document Migration.	From \$5,995 USD					High	Full




Option 1

Cross-Tenant SharePoint Migration

►► Option 1 | Cross-Tenant SharePoint Migration

The diagram below outlines the method for migrating the SharePoint Site Collection out of Project Online.

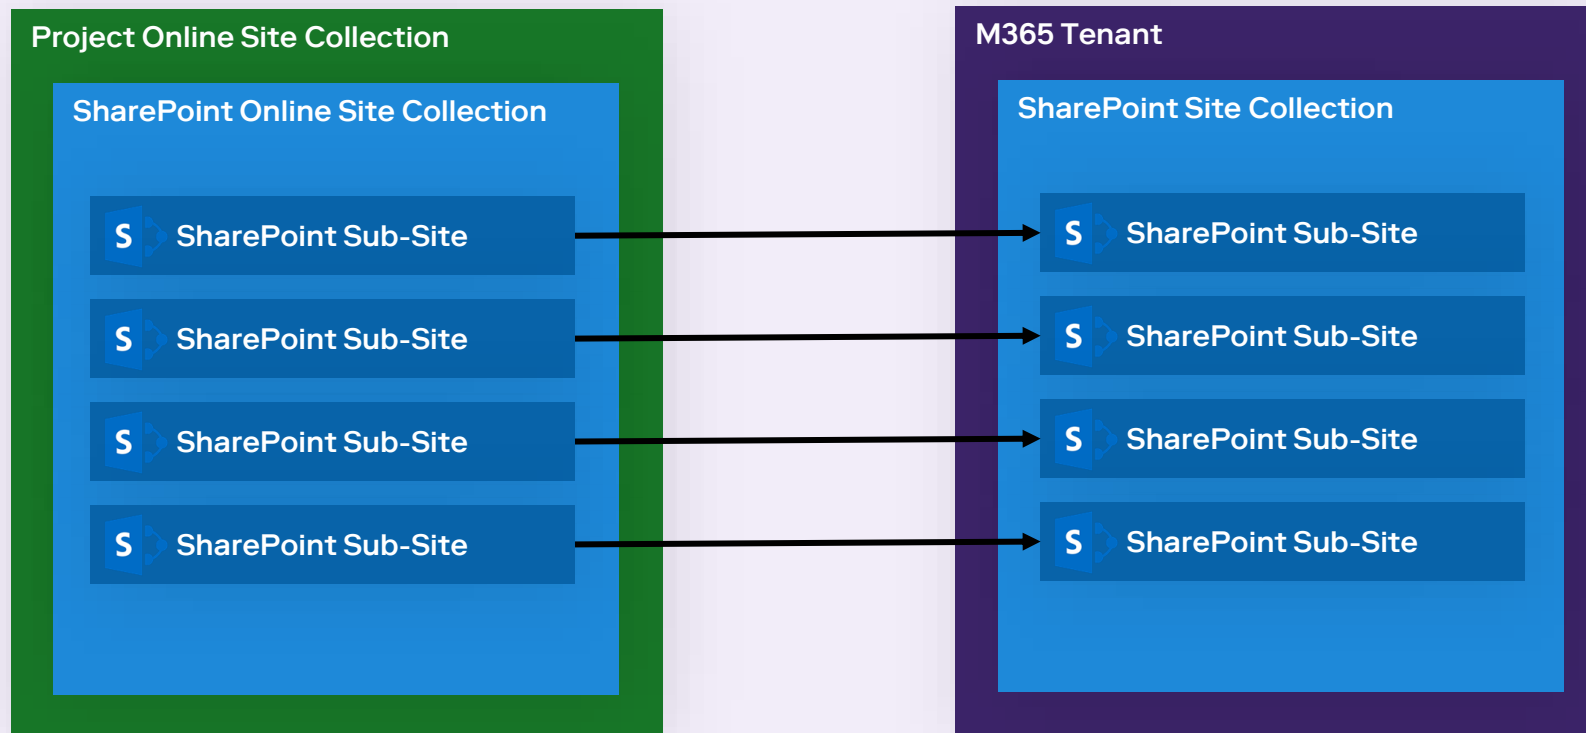

- The approach utilizes the Microsoft Cross-tenant SharePoint migration process.
- The entire SharePoint Site collection will be moved to another site collection within the M365 Tenant.
- This will ensure that these sub-sites are still available after Microsoft decommissions Project Online.
- Once the SharePoint Site Collection has been migrated, there is a simple step in Altus required to complete the process.

► Option 1 | Cross-Tenant SharePoint Migration

The diagram below outlines the method for migrating the SharePoint Site Collection out of Project Online.

#	Step	Details
1	Connect to Tenants	▪ Connect to both the source and target tenants using SharePoint Management Shell. ▪ Step 1 Connect to Tenants
2	Establish Trust between Tenants	▪ Run commands via PowerShell to establish trust between both the source and target tenants. ▪ Step 2 Establish trust between the tenants
3	Verify trust between the tenants	▪ Run PowerShell commands to verify that trust has been established. ▪ Step 3 Verify trust between the tenants
4	Pre-create users & groups	▪ Process to create users and groups in the target tenant's directory. ▪ Step 4 Pre-create users & groups
5	Prepare the identity mapping file	▪ Create a single CSV file that contains the mapping of users and groups between tenants. ▪ Step 5 Prepare the identity mapping file
6	Start the cross-tenant SharePoint migration	▪ Start the cross-tenant migration process using PowerShell. ▪ Step 6 Start the cross-tenant SharePoint migration
7	Post migration steps	▪ Run Microsoft Steps, add new SharePoint Site URL into Altus. ▪ Step 7 Post migration steps


ALTUS

Option 2

**Power Automate
approach**

►► Option 2 | Power Automate Approach

The diagram below outlines the method for migrating documents into Altus using Power Automate.




The approach above is designed to work with the OOTB groups and teams in Altus.
If additional document metadata needs to be migrated, this process can be updated to accommodate it.

</> Option 2 | Power Automate Approach

The diagram explains in more detail how the migration approach will migrate the document.

 Connect to SharePoint and retrieve projects and document libraries

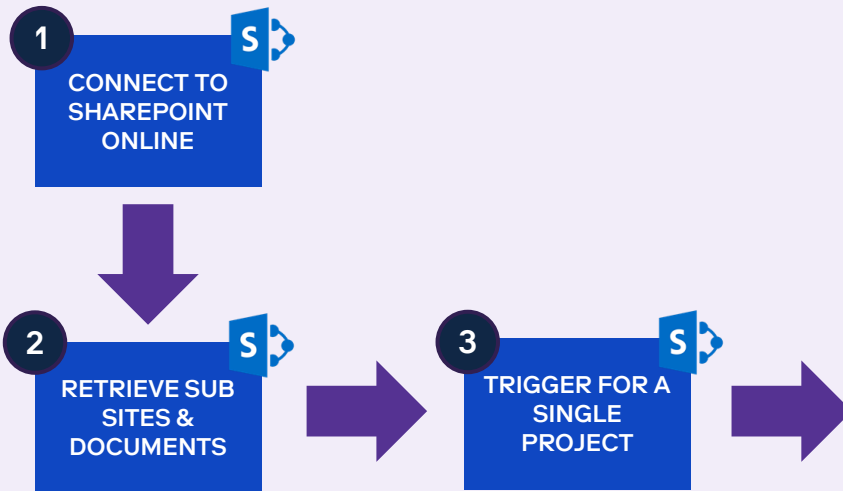

This migration approach is designed to be run on a per-project basis and will copy the documents to the relevant group/team. This will enable Partners and Customers to determine how best to run these scripts without committing to a 'big bang' approach.

 Copy documents for a single project



</> Option 2 | Power Automate Approach

Migration of SharePoint Online documents

#	Step	Details
1	Connect to SharePoint Online	The first Power Automate flow will connect to the source SharePoint Online environment.
2	Retrieve Sub-Sites and Document Libraries	Once connected, it will retrieve all sub-sites and the document libraries within these sub-sites.
3	Trigger for a Single Project	The migration script is triggered for a single project.
4	Retrieve Documents & Metadata	The script will retrieve the documents and their associated metadata for the selected project.
5	Connect to Altus Group	Then it will connect to the target project in Altus and its Group.
6	Copy Documents & Metadata	The documents and their associated metadata will be created in the Group.


ALTUS

Option 3

**Share Gate
approach**

►► Option 3 | Share Gate Approach

The diagram below outlines the method for migrating documents into Altus using Share Gate

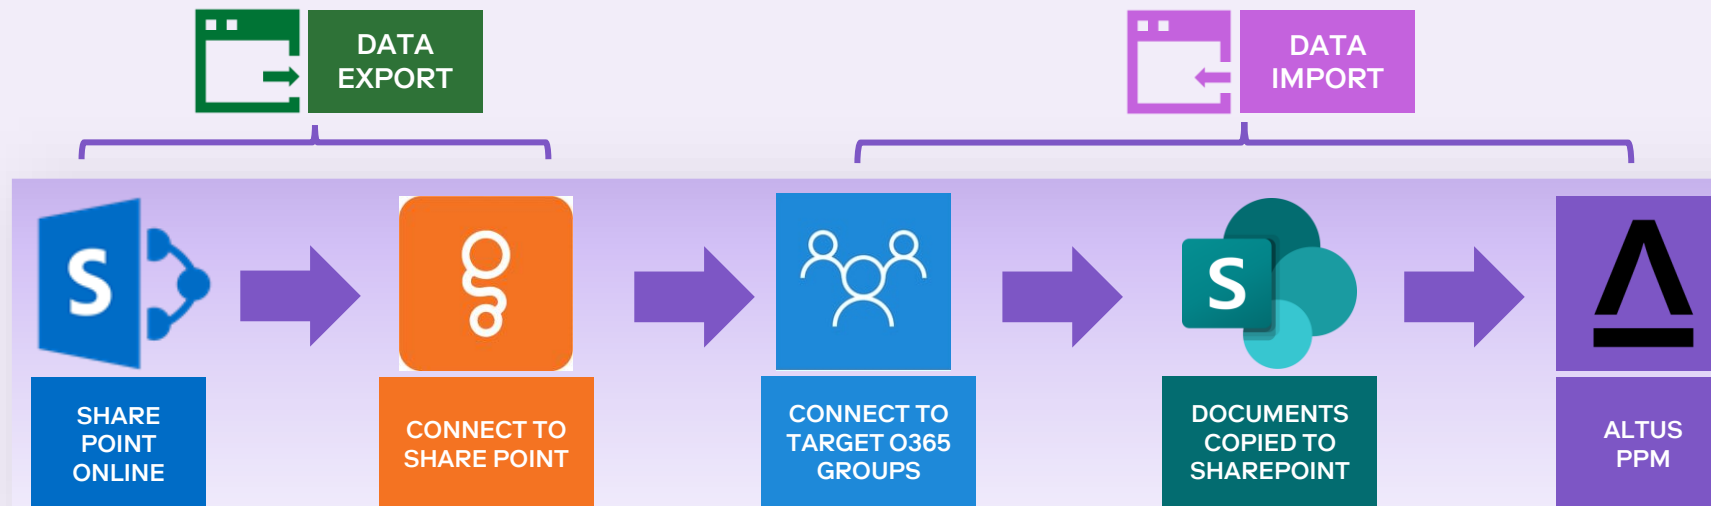

The approach above utilizes a proprietary tool Share Gate to copy the documents, metadata, and version history from SharePoint Online to the O365 Groups and document libraries structure that Altus uses.

►► Option 3 | Share Gate Approach


The diagram explains in more detail how the migration approach will migrate the document.



Connect to SharePoint Online & retrieve all metadata and versions



Copy documents



</> Option 3 | Share Gate Approach

Migration of SharePoint Online documents

#	Step	Details
1	Connect to SharePoint Online	Share Gate will connect to the SharePoint site collection and will connect to all sub-sites.
2	Retrieve Documents & Metadata	Share Gate will retrieve the documents and their associated metadata for the selected sub-sites.
3	Connect to Altus Group	Then it will connect to the target Altus environment and the groups.
4	Copy Documents & Metadata	The documents and their associated metadata will be created in the Groups.



Data Migration Support

Migration Support | Overview

What support will we provide to Partners and Customers migrating from Project Online to Altus?

Support	Details
 Migration Tools & Approach	▪ Altus will provide tools and an approach for Partners and Customers who wish to migrate from Project Online to Altus. ▪ These tools will be provided as part of the Altus subscription.
 Videos & 'How To' Guides	▪ Altus will provide videos and how to guides covering the end-to-end migration documented in this pack. ▪ Note, these will guide Partners and Customers through the Altus approach. Any changes to this approach would need to be complimented with materials by Partners (where they are assisting their clients directly).
 Email Support	▪ Altus will respond to questions regarding the approach documented in this pack. ▪ This will be responding to questions about steps documented in this pack. ▪ Note: Any changes or modifications to tools and scripts which result in questions will need to be managed by Altus Partners. ▪ 'Call me' option for Partners and support channel.

Migration Support | Videos & Guides

What videos & guides will be created to support our Partners and Customers during the migration from Project Online to Altus?


Materials	Details
One Pager End-to-end Process	Simple 'on a page' guide to the migration and the outcomes it enables for Partners and Customers.
How To Guide Schedule Migration	Detailed guide for how to complete the schedule migration – Procedural with screenshots.
How To Guide List Data Migration	Detailed guide for how to complete the list data migration – Procedural with screenshots.
How To Guide Document Migration	Detailed guide for how to complete the document migration – Procedural with screenshots.
One Pager Prerequisites	One pager explaining how to address the migration prerequisites.
Video Schedule Migration	Video walkthrough on an example migration (to support the detailed how to guide).
Video List Data Migration	Video walkthrough on an example migration (to support the detailed how to guide).
Video Document Migration	Video walkthrough on an example migration (to support the detailed how to guide).



POL Migration Delivery Plan

►► Development Streams

The visual explains how we will organise development work for POL migration.

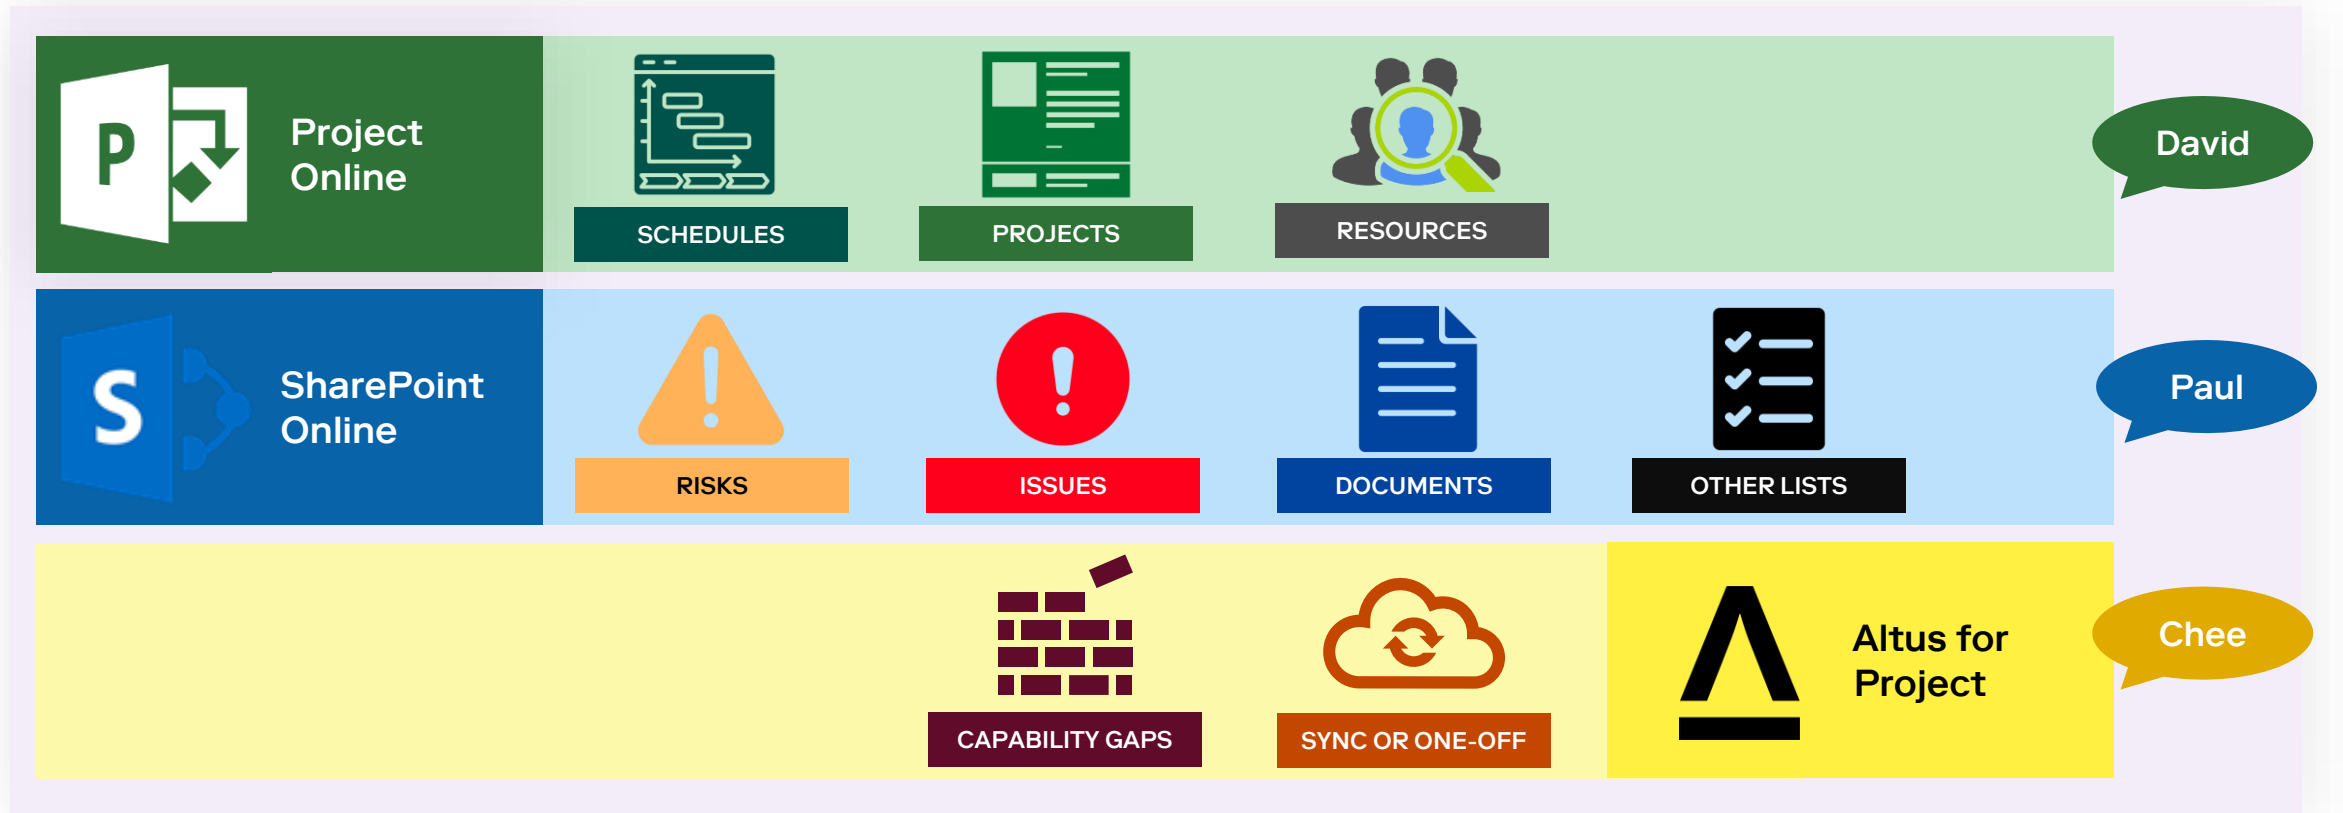

»» So Far...

- ❖ V1 – passed testing
 - Ready for pilot use
 - Documentation needed
- ❖ GREEN stream
 - Tickets are created for migrating Custom Fields
 - Dev work has started
- ❖ YELLOW stream
 - Tickets are created for migrating Baselines
 - Ticket is created for migrating Resource Rates
 - Alignment scheduled for Wednesday
- ❖ BLUE stream
 - Alignment scheduled for later today



ALTUS

Questions?
